



The Township Center Project - 2020

SUBJECT: DAILY DIARY September 03, 2020

WEATHER: 70's and 80's degrees, and sunny.

WORK DAY = 64.

E. P. DOYLE: Graham on-site all day.

PREMIUM: +5

COM ED: +3

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today:

- Premium finished preparations.
- Premium placed concrete in the diamond and the stairs and the triangles.
- Com Ed on-site to wrap the wires.

Activities Planned for Friday:

- Premium Concrete on-site tomorrow, to complete the diamonds and the stairs.

Activities Planned for Tuesday:

- Premium Concrete, to pour the first floor 2" first floor topping.

Critical Path:



- Get the steel complete and off the site.

Pending Items:

-

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

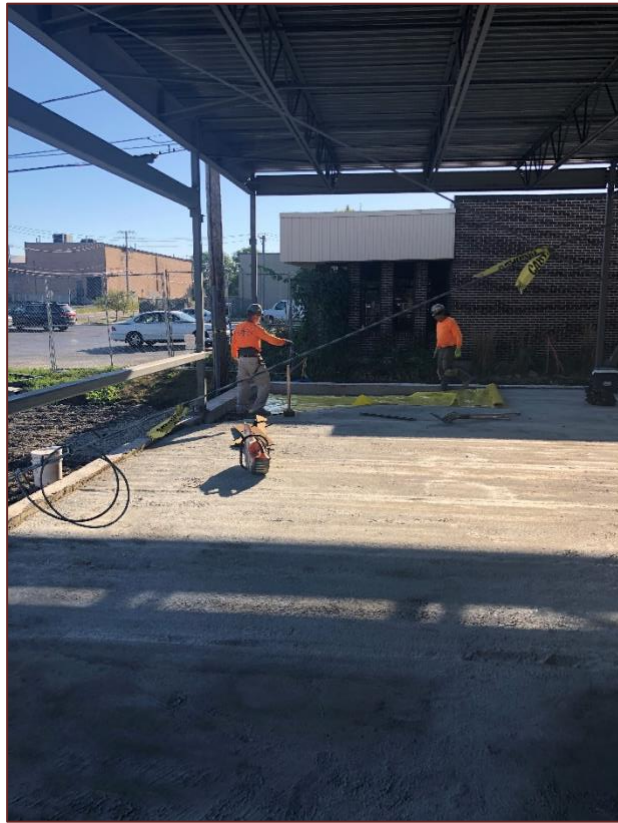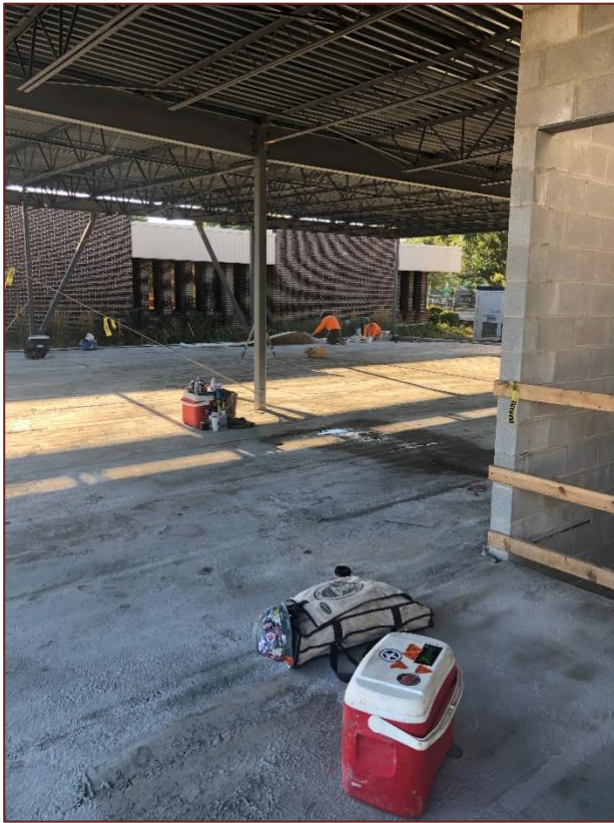


Prepping for concrete.




Com Ed.



Rubbered wires.

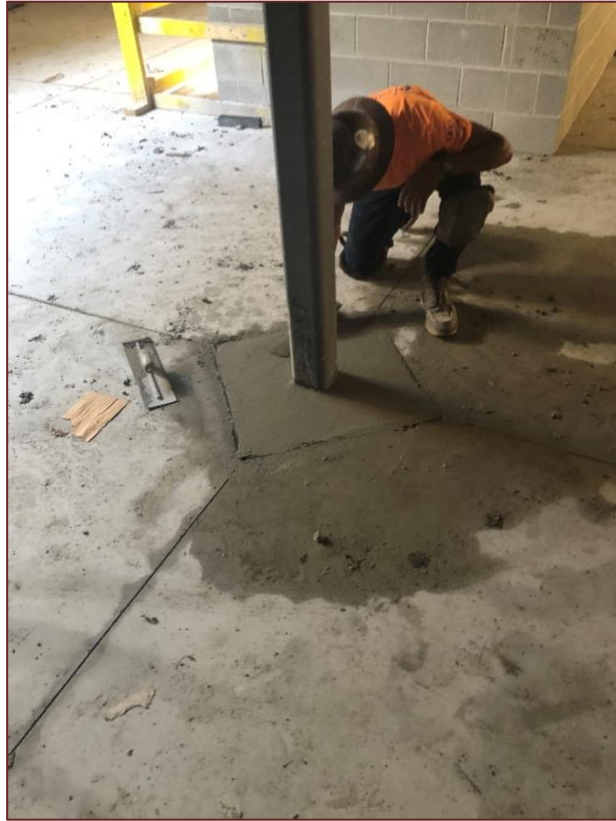

Placing the diamonds.

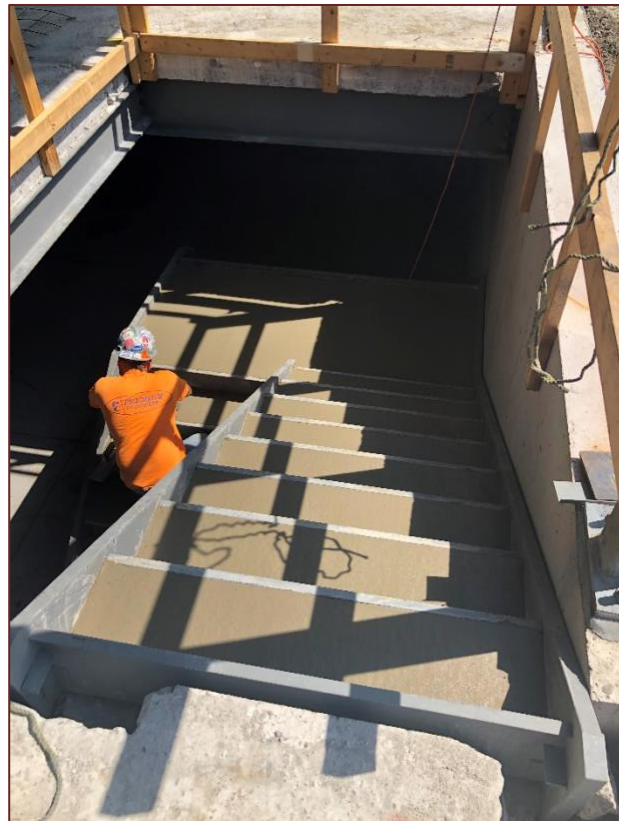

Chuting the concrete and placing the stairs.
