



The Township Center Project - 2020

SUBJECT: DAILY DIARY July 06, 2020

WEATHER: 80's & 90's degrees, sunny and hot.

WORK DAY = 22.

E. P. DOYLE: On-Site Tony; all day.

ENGINEERING SOLUTIONS TEAM: Ed on-site on and off during the day.

WALKER: Jose and Damon and Bob Jr. on-site today.

Activities Today:

- Walker on-site completed the restoration of the basement sub-grade to its proper elevation. Clean gravel was used. 6 trucks were brought on-site today.

Activities Tuesday:

- Premium will be on-site to begin framing the basement walls. According to Tony this afternoon – Premium will place concrete for the east and south and west walls on Friday.


Pending Items:

- ---

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020

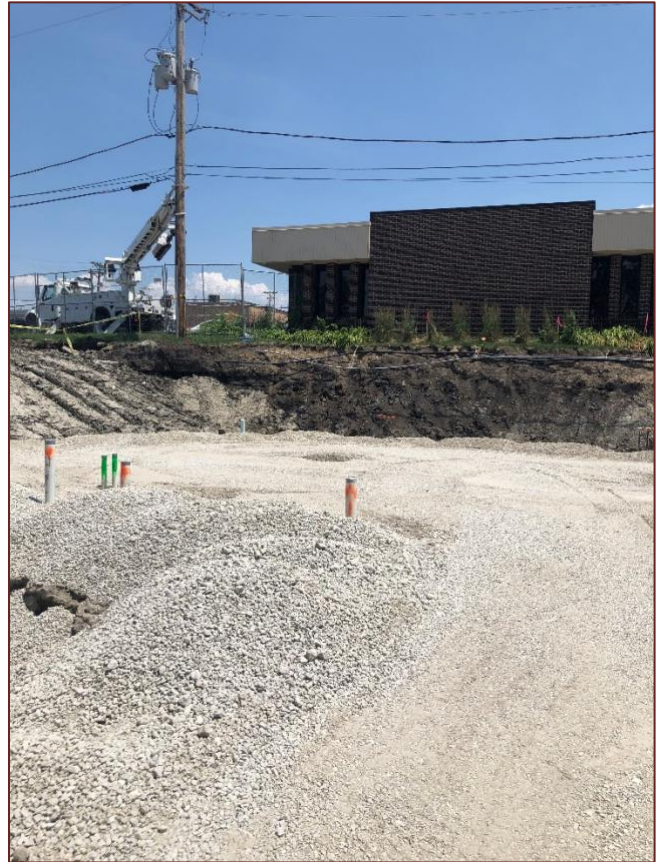

Completing the sub-base for the Basement.



Completing the sub-base for the Basement.
