



The Township Center Project - 2020

SUBJECT: DAILY DIARY July 31, 2020

WEATHER: 70's - 80's degrees, mostly sunny.

WORK DAY = 40.

E. P. DOYLE: On-Site Tony all day. Tim and Ed on-site this morning.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

OLD STYLE STEEL: +6 on-site.

Activities Friday:

- Begin setting the steel columns and beams.

Activities Monday:

- Continue setting the steel.

Critical Path:

- Delivery and installation of the pre-cast floor planks.
- Backfill around the outside of the basement walls.

Pending Items:

- -----

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.




Setting the steel. .



Setting the steel.

The Township Center Project - 2020

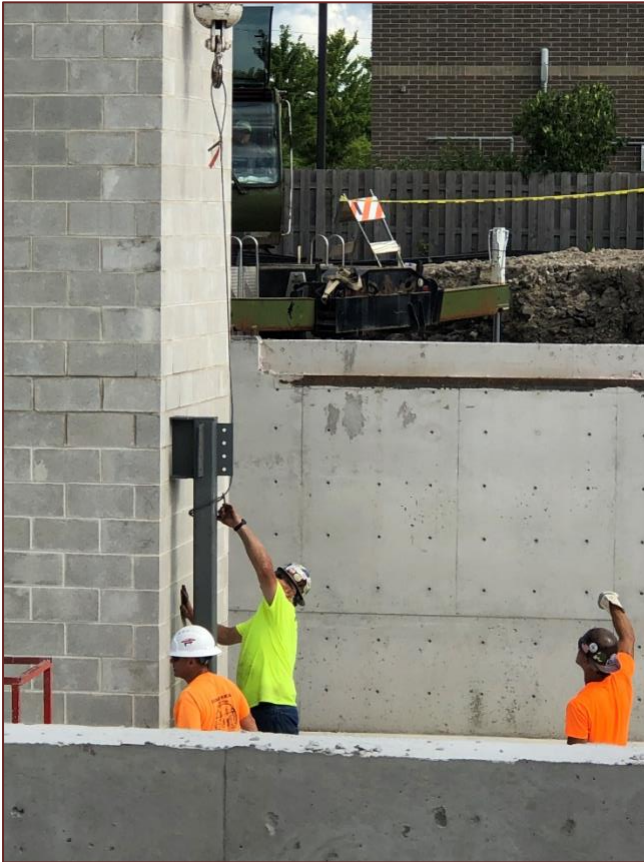

Setting the steel..



Setting the steel.
