



# The Township Center Project - 2020



SUBJECT: DAILY DIARY August 11, 2020

WEATHER: 80's degrees, sunny.

WORK DAY = 47.

E. P. DOYLE: On-Site Tony all day.

WALKER: Jose and Jack on-site all day

ENGINEERING SOLUTIONS TEAM: Ed on-site.

### Activities Today:

- Walker worked on backfilling the outside of the basement walls.
- Trucks of CA 6 delivered to the site.

### Activities Planned for tomorrow:

- Walker to continue backfilling the outside of the basement walls.
- Premium Concrete to be on-site and begin constructing the east corner foundations.

### Critical Path:


- Backfill around the outside of the basement walls.
- Remove the Com Ed Truck.

### Pending Items:

- -----

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

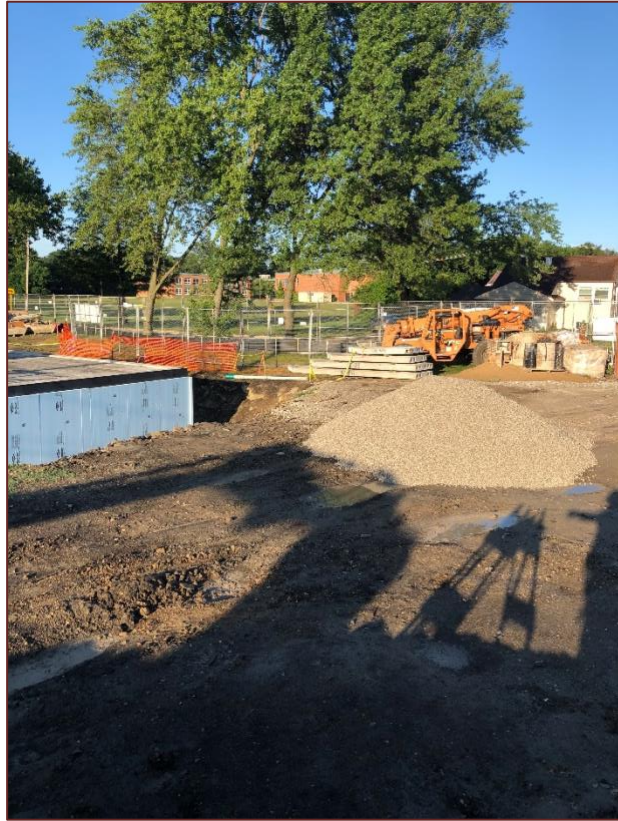

Starting the day.



Backfilling the outside of the basement walls.
