



The Township Center Project - 2020



SUBJECT: DAILY DIARY August 26, 2020

WEATHER: 80's and 90's degrees, sunny.

WORK DAY = 58.

E. P. DOYLE: On-Site, Graham all day. Ed in the morning.

OLD STYLE: +3

CARPENTER: +1

WALKER: +2

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today:

- Old Style on-site today, working on welding.
- Carpenter on-site to perform preliminary measurements.
- Waiting on Com Ed regarding the wiring.
- Walker straightened up the silt fence.
- Doyle submitted the compaction tests to the Village.
- Ed obtained the Fire and safety permit from the Village.

Activities Planned for Thursday:

- Old Style to continue the detailing of the first-floor steel.
- EP Doyle to re-submit the spot survey to the Village.

Critical Path:


- Cover the wires?

Pending Items:

- -----

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

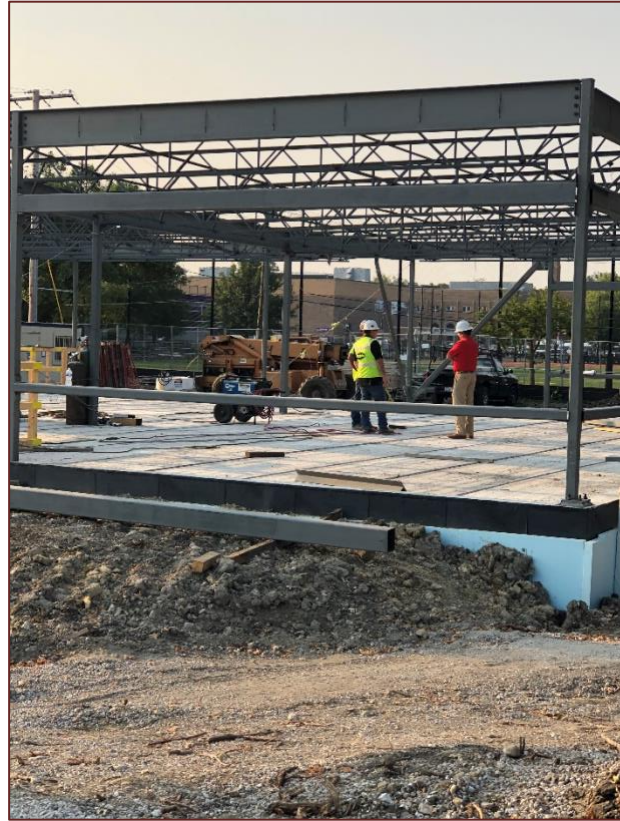

Getting started today.



Carpenter layout.



Refurbished silt fence.
