



The Township Center Project - 2020



SUBJECT: DAILY DIARY September 16, 2020

WEATHER: 60's and 70's degrees and sunny.

WORK DAY = 68 + 1 = 69.

E. P. DOYLE: Graham on-site all day. Ed on-site.

CALIBER: +4.

NELSON: +3.

STANTON: +2.

TALON: +2.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today:

- Caliber = worked on exterior framing.
- Nelson = Continued installing the lower level water safety pipes.
- Stanton = Starts plumbing.
- Talon = installs the temp electric in the basement.
- Doyle = performed site clean-up

Activities Planned for Wednesday:

- Caliber on-site.
- Nelson on-site.
- Old Style on-site.

Critical Path:

- Complete the shop drawings.

Pending Items:

- Get Com Ed on-site to nail down the exact source of the service.

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.




Getting Started.



Fire Safety System install in the basement.



Site Cleanup.

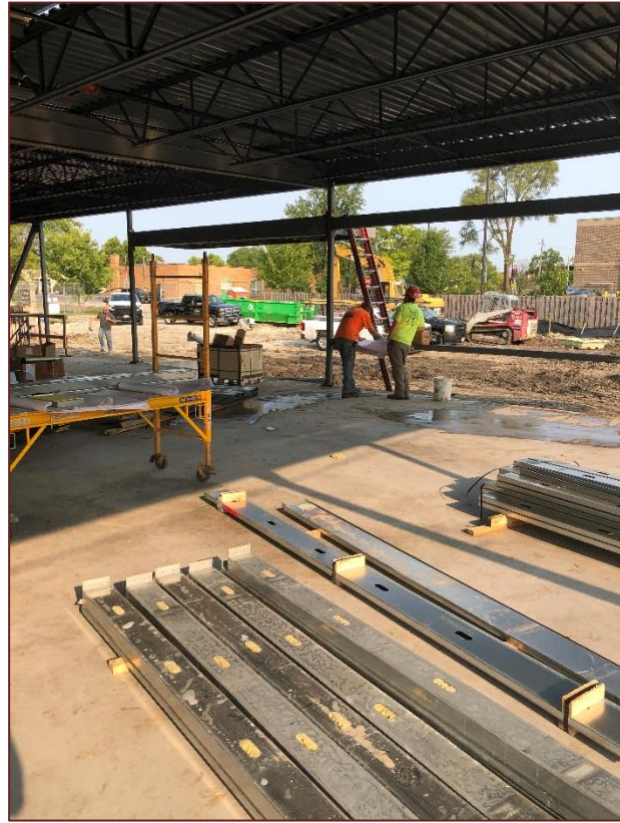

Work on first floor.
