



SUBJECT: DAILY DIARY September 17, 2020

WEATHER: 60's and 70's degrees and sunny.

WORK DAY = 69 + 1 = 70.

E. P. DOYLE: Graham on-site all day. Ed on-site.

CALIBER: +4.

J B MECHANICAL: +2.

OLD STYLE: Jim.

TALON: +2.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today:

- Caliber = worked on exterior framing.
- J B Mechanical = Begins installing the first floor HVAC.
- Old Style = Correctly installed the stair railings.
- Talon = completes the install of the temp electric in the basement.

Activities Planned for Friday:

- Caliber on-site.
- J B Mechanical on-site.

Critical Path:

- Notify the Village and DGSD of Archon's pending work.

Pending Items:

- Get Com Ed on-site to nail down the exact source of the service.

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.


The Township Center Project - 2020



Getting Started.



HVAC Materials on-site.

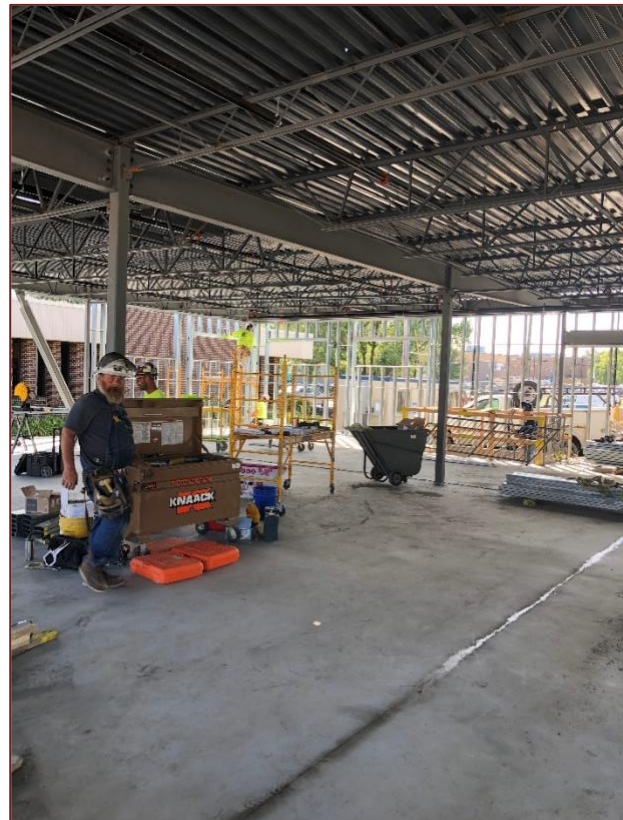

Carpenters work.



Lighted basement.



Stair rail.



HVAC work.
