



# The Township Center Project - 2020

---



SUBJECT: DAILY DIARY September 18, 2020

WEATHER: 60's and 70's degrees and sunny.

WORK DAY = 70 + 1 = 71.

E. P. DOYLE: Graham on-site all day.

CALIBER: +4.

J B MECHANICAL: +2.

TALON: +2.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

### Activities Today:

- Caliber = worked on exterior framing.
- J B Mechanical = Installing the first floor HVAC and on the roof.
- Talon = begins installing conduit in the basement.

### Activities Planned for Next Week:

- Com Ed to communicate about the proposed service.
- Carpenters framing to continue.
- Electrical installations to continue.
- Plumbing work to begin.
- HVAC work to continue.
- Archon to coordinate with the Village and DGSD regarding the pending installation of services.

### Critical Path:

- Notify the Village and DGSD of Archon's pending work.

### Pending Items:

- Get Com Ed on-site to nail down the exact source of the service.

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

# The Township Center Project - 2020




Getting Started.



Electrical Installation in the basement.



Carpenters work.

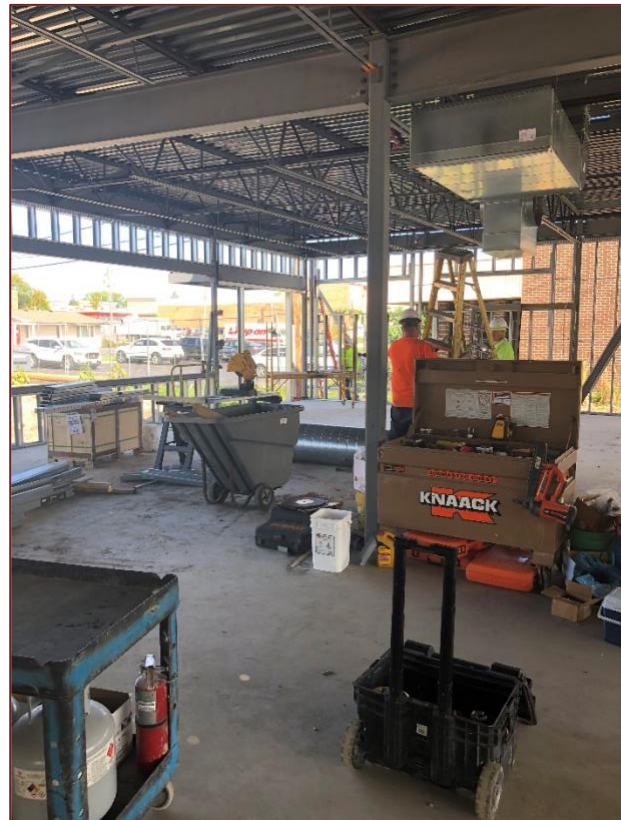





HVAC work.



West elevation.



South elevation.
