



The Township Center Project - 2020



SUBJECT: DAILY DIARY September 28, 2020

WEATHER: 60's degrees overcast and rainy.

WORK DAY = 77.

E. P. DOYLE: Graham on-site all day.

CALIBER: +0.

J B MECHANICAL: +0.

TALON: +3.

STANTON: +3.

PREMIUM: +2.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today:

- Talon = begins installing the lighting in the basement.
- Stanton = working on plumbing for bathrooms on first floor.
- Premium = Finishes the first floor concrete finish.

Activities Planned for Tomorrow:

- Carpenters back on-site.
- Electrical installations to continue.
- Plumbing work to continue.
- Archon to install the sanitary sewer service.

Critical Path:

- Install the Services.

Pending Items:

- Get Com Ed on-site to nail down the exact source of the service.

Please advise if there are questions or if I missed anything.


Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.




North Elevation.



West Elevation.

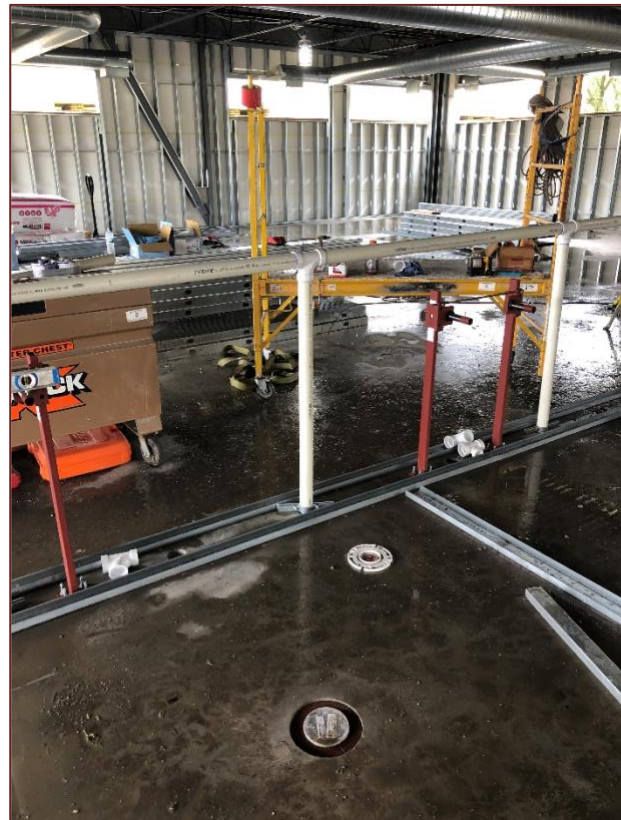

Plumbers on first floor.

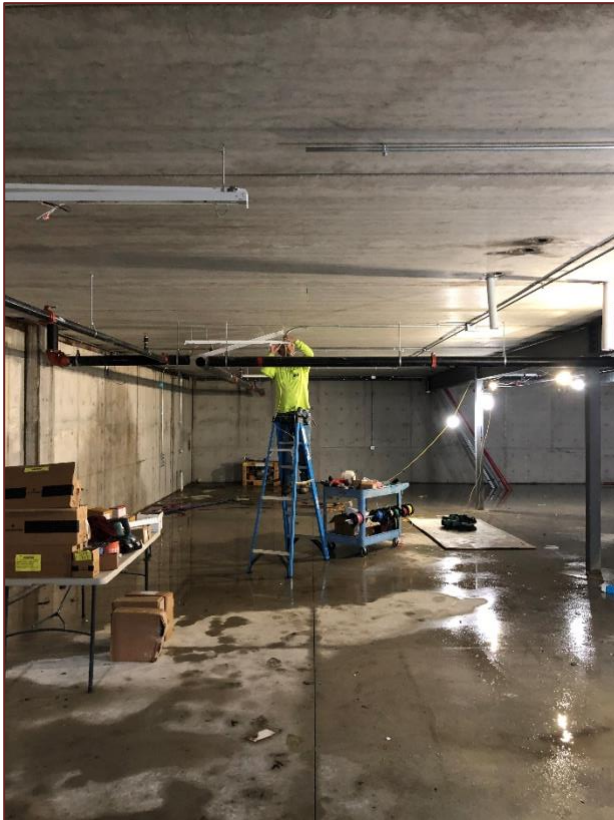

Electricians in the lower level.



Finished concrete first floor.
