



The Township Center Project - 2020



SUBJECT: DAILY DIARY September 30, 2020

WEATHER: 50's and 60's degrees, overcast.

WORK DAY = 79.

E. P. DOYLE: Graham on-site all day and Ed on-site.

TALON: +1.

STANTON: +3.

CALIBER: +4.

OLD STYLE: +2.

IWS: +2.

IBBEN: +2.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today:

- Talon = continues installing the lighting in the basement.
- Stanton = continues working on plumbing for bathrooms on first floor.
- IWS = works on installing the building water proofing and air barrier.
- Com Ed = located the new pole for the drop. Ed called Javon to ask if another pole was really required for the drop.
- Old Style = works on detailing the stair rails.
- Caliber = continues working on the first floor walls.
- Ibben = built the brick wall mock up.

Activities Planned for Tomorrow:

- Carpenters back on-site.
- Electrical installations to continue.
- Plumbing work to continue.

Critical Path:

- Install the Water and Gas Services.

Pending Items:

- Get Com Ed on-site to nail down the exact source of the service.


Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020




Work on the outside walls.

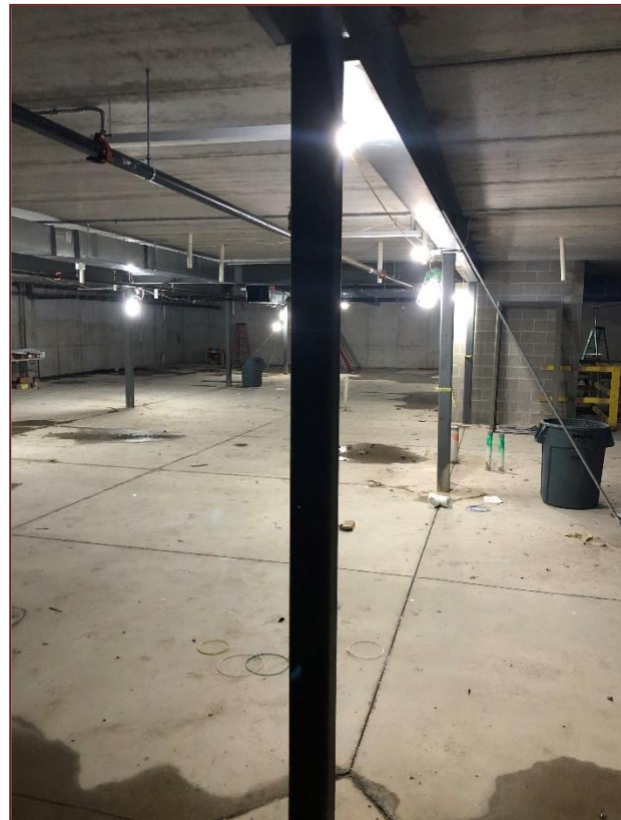

Working in the basement.



The brick mock up.

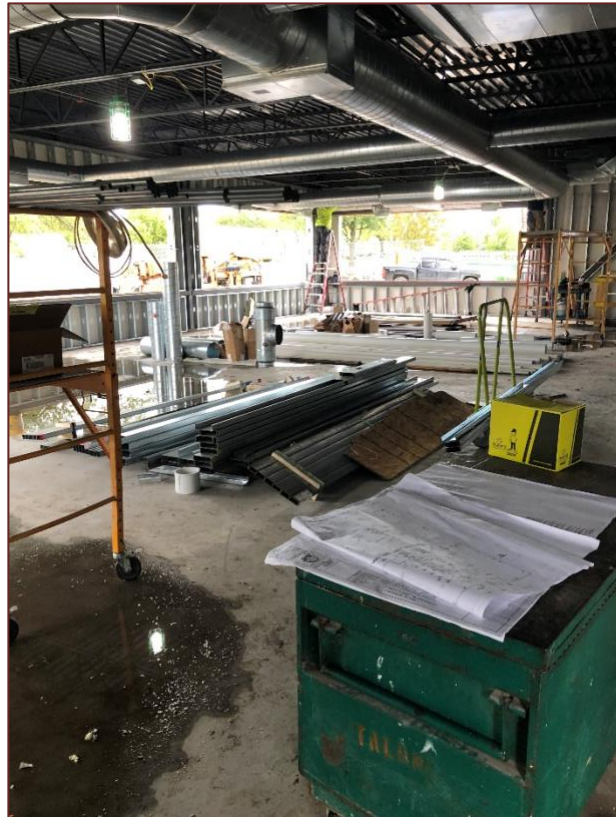

Work on first floor.
