



The Township Center Project - 2020



SUBJECT: DAILY DIARY October 1, 2020

WEATHER: 50's and 60's degrees, variable.

WORK DAY = 80.

E. P. DOYLE: Graham on-site all day and Russ on-site for meeting with ADT.

TALON: +2.

STANTON: +3.

CALIBER: +1.

IWS: +2.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today:

- Talon = installing conduit on first floor.
- Stanton = continues working on plumbing for bathrooms on first floor.
- IWS = works on installing the building water proofing and air barrier.
- Caliber = continues working on the first floor walls.
- Security planning meeting with ADT.

Activities Planned for Tomorrow:

- Carpenters back on-site.
- Electrical installations to continue.
- Plumbing work to continue.
- IWS to continue work on water proofing and air barrier.

Critical Path:

- Install the Water and Gas Services. Water service install scheduled for Monday

Pending Items:

- Get Com Ed on-site to nail down the exact source of the service.


Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020



Plumbers working.

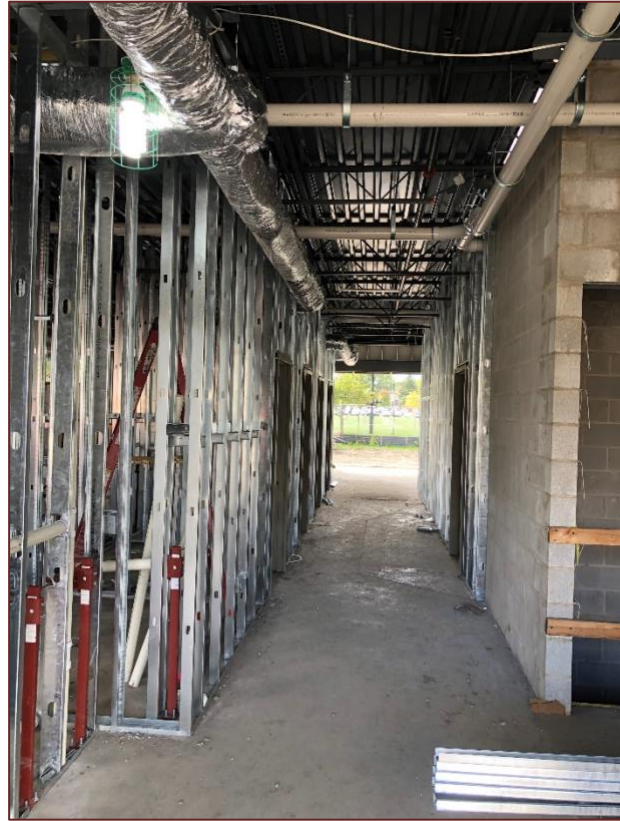

The main hallway.



The sanitary sewer connection to the building.





The new Com Ed pole location.



The east elevation.



The south elevation.



The west elevation
