



The Township Center Project - 2020



SUBJECT: DAILY DIARY October 2, 2020

WEATHER: 50's and 60's degrees, sunny.

WORK DAY = 81.

E. P. DOYLE: Ed was on and off site today.

TALON: +2.

STANTON: +3.

CALIBER: +2.

IWS: +2.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today:

- Talon = installing conduit on first floor.
- Stanton = continues working on plumbing for bathrooms on first floor.
- IWS = works on installing the building water proofing and air barrier.
- Caliber = continues working on the first floor walls.
- Mark approves the brick and mortar mock up.

Activities Planned for Early next week:

- Carpenters are finishing up.
- Electricians are finishing up.
- Plumbing work is finishing up.
- IBEN to begin this week.
- Archon to begin watermain on Monday

Critical Path:

- Install the Water and Gas Services. Water service install scheduled for Monday

Pending Items:


Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020



The north elevation.

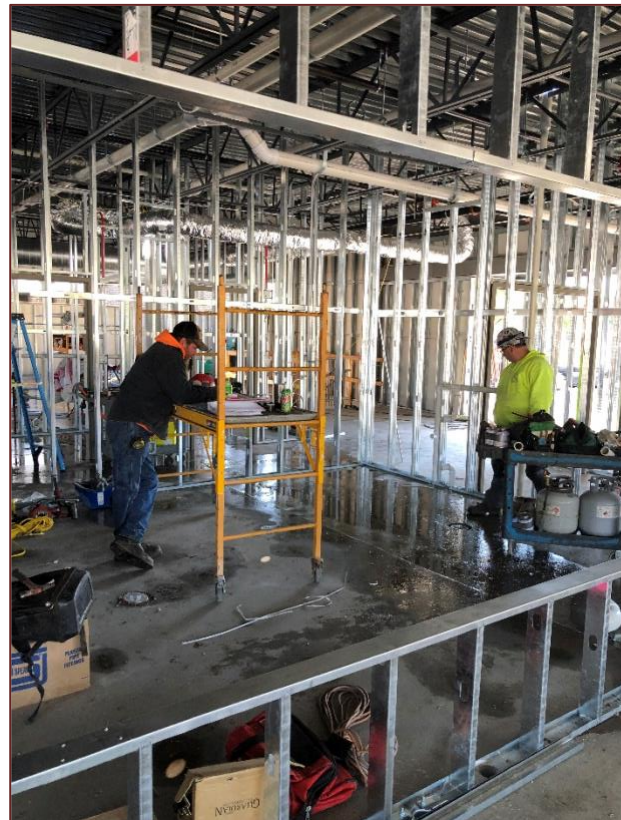

The plumbers work.



The basement.



The door frames.
