



The Township Center Project - 2020



SUBJECT: DAILY DIARY October 6, 2020

WEATHER: 50's and 60's degrees, sunny.

WORK DAY = 83.

E. P. DOYLE: Graham on site today.

TALON: +2.

STANTON: +3.

CALIBER: +3.

ARCHON: +5

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today:

- Talon = installing conduit on first floor.
- Stanton = continues working on plumbing for bathrooms and kitchen on first floor.
- Caliber = continues working on the first floor walls.
- Archon = constructs the water service.

Activities Planned for Tomorrow:

- Carpenters are finishing up.
- Electricians are finishing up.
- Plumbing work is finishing up.
- IBBEN to begin next week.
- Archon to connect to the Village watermain.
- Roofers to start.

Critical Path:

- Install the Water and Gas Services. Water service install scheduled for Tuesday.
- Better understand the kitchen plan.
- Install the masonry.

Pending Items:

- Get NICOR scheduled.

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.


The Township Center Project - 2020



Starting the day.



The community room.

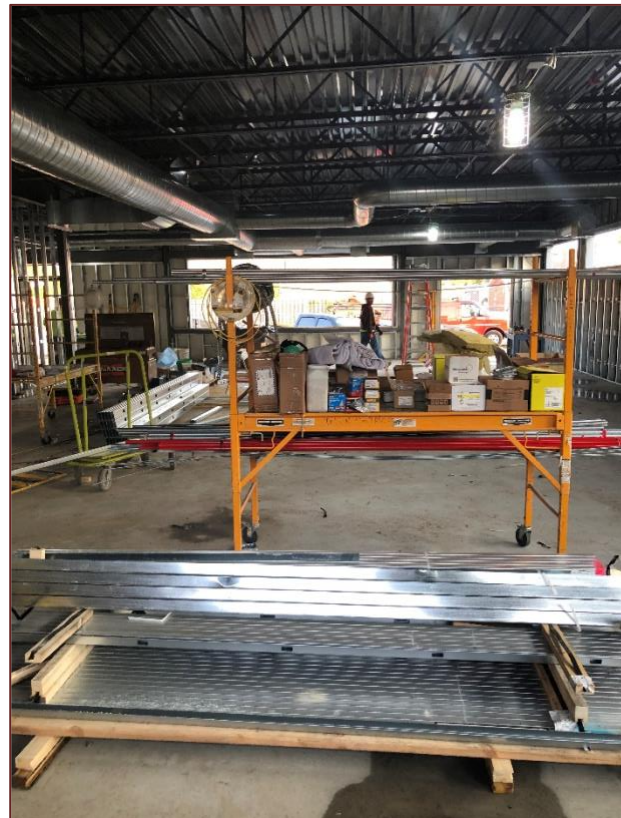

The work room.

The Township Center Project - 2020



The water service entrance to building.



Today's work.
