



The Township Center Project - 2020



SUBJECT: DAILY DIARY October 7, 2020

WEATHER: 60's and 70's degrees, sunny.

WORK DAY = 84.

E. P. DOYLE: Graham on site today. Russ attends Kitchen coordination meeting.

TALON: +2.

METAL MASTERS: +4.

STANTON: +3.

CALIBER: +3.

ARCHON: +4

OLD STYLE: Jim.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today:

- Talon = installing conduit on first floor.
- Stanton = continues working on plumbing for bathrooms and kitchen on first floor.
- Caliber = continues working on the first floor walls.
- Archon = connects the water service.
- Metal Masters = starts working on the roof.
- Old Style = Cuts the floor to construct the stairwell walls.
- Mark and Russ and Ed meet to discuss Kitchen details: including a new drain under the warming table, 2 new outlets on the north wall and 2 outlets in the meeting room for TV's.

Activities Planned for Tomorrow:

- Carpenters are finishing up.
- Electricians are finishing up.
- Plumbing work is finishing up.
- IBEN to begin next week.
- Roofers now on-site.

Critical Path:

- Better understand the kitchen plan.

Pending Items:

- Get NICOR scheduled.

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020




Starting the day.



Connecting to the watermain.



The working room.

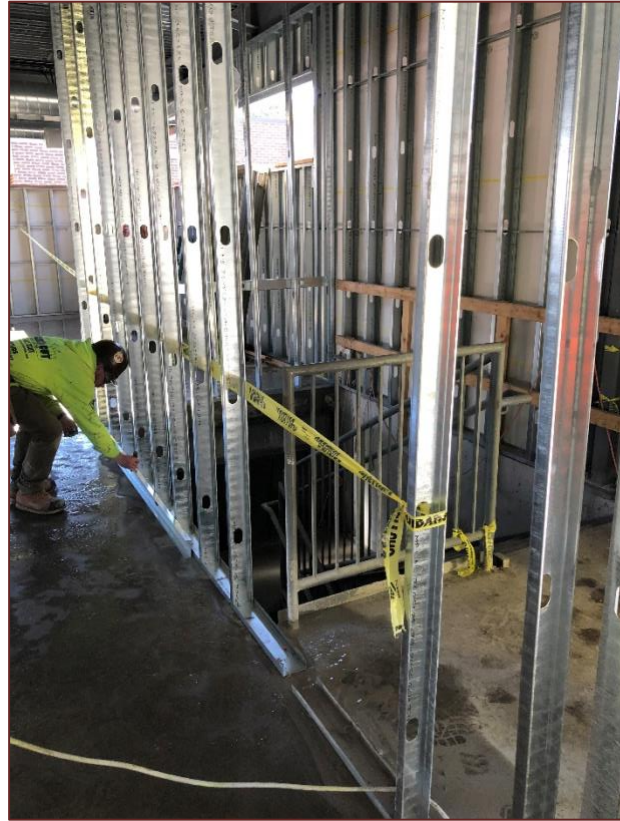

Encasing the south stairwell.
