



The Township Center Project - 2020



SUBJECT: DAILY DIARY October 8, 2020

WEATHER: 60's and 70's degrees, sunny.

WORK DAY = 85.

E. P. DOYLE: Graham on site today. Ed on-site.

TALON: +2.

METAL MASTERS: +4.

STANTON: Don.

CALIBER: +1.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today:

- Talon = installing conduit on first floor.
- Stanton = continues working on plumbing in the basement.
- Caliber = continues working on the first floor walls.
- Metal Masters = working on the roof.

Activities Planned for Tomorrow:

- Carpenters are finishing up.
- Electricians are finishing up.
- Plumbing work is finishing up.
- IBEN to begin next week.
- Roofers on-site.

Critical Path:

- Better understand the kitchen plan.

Pending Items:

- Get NICOR scheduled.

Please advise if there are questions or if I missed anything.


Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.



Basement sanitary pipe.




1st floor.

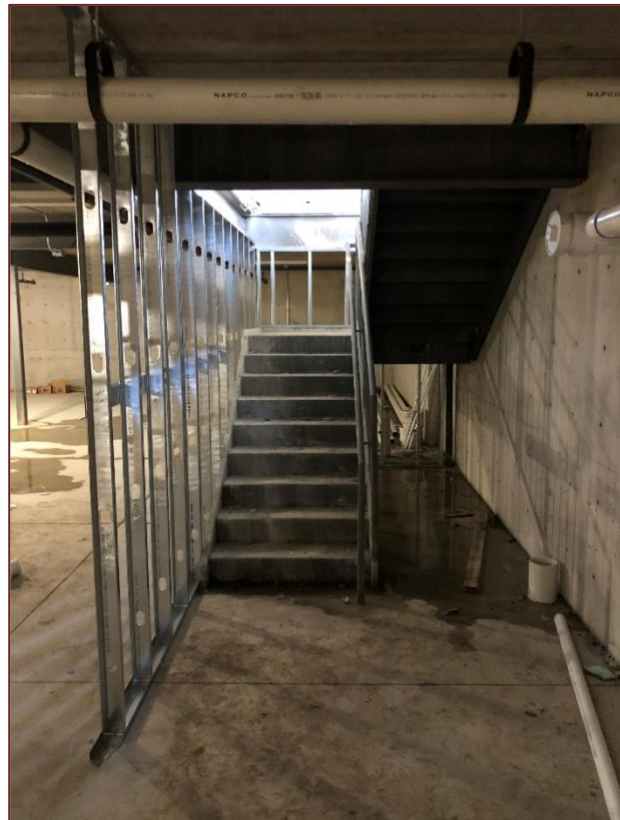

Basement door?

The Township Center Project - 2020

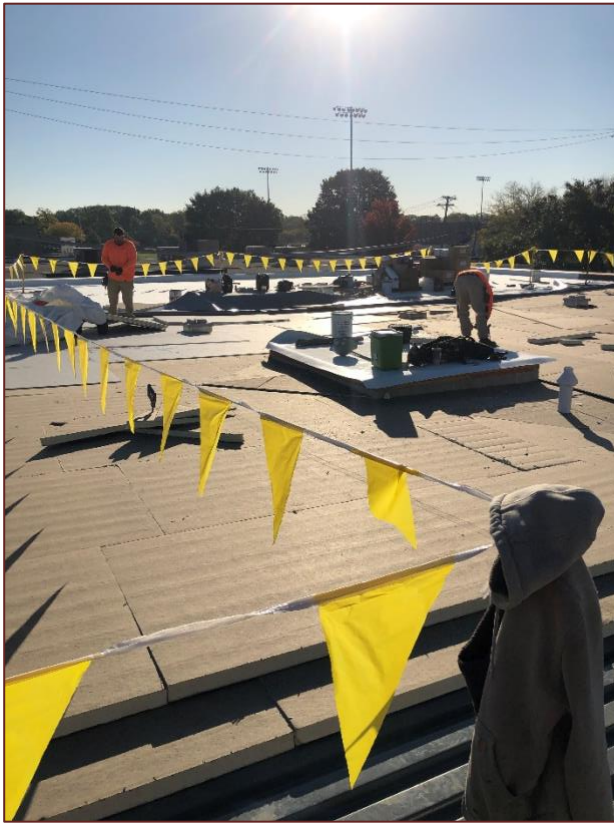

The roof work.



The roof work..
