



## The Township Center Project - 2020

---



SUBJECT: DAILY DIARY October 9, 2020

WEATHER: 60's and 70's degrees, sunny.

WORK DAY = 86.

E. P. DOYLE: Graham on site today. Russ on-site for meetings.

TALON: +1.

METAL MASTERS: +4.

STANTON: 1.

CALIBER: +1.

MTZ: Ed on-site for meetings.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

### Activities Today:

- Talon = installing conduit on first floor.
- Stanton = continues working on plumbing in the basement.
- Caliber = continues working on the first floor walls.
- Metal Masters = working on the roof.
- Project team meeting and site inspection.

### Activities Planned for Monday:

- Carpenters are finishing up.
- Electricians are finishing up.
- Plumbing work is finishing up.
- Bricks to start being delivered.
- Roofers on-site.

### Critical Path:

- Masonry work.


### Pending Items:

- Get NICOR scheduled.

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

# The Township Center Project - 2020

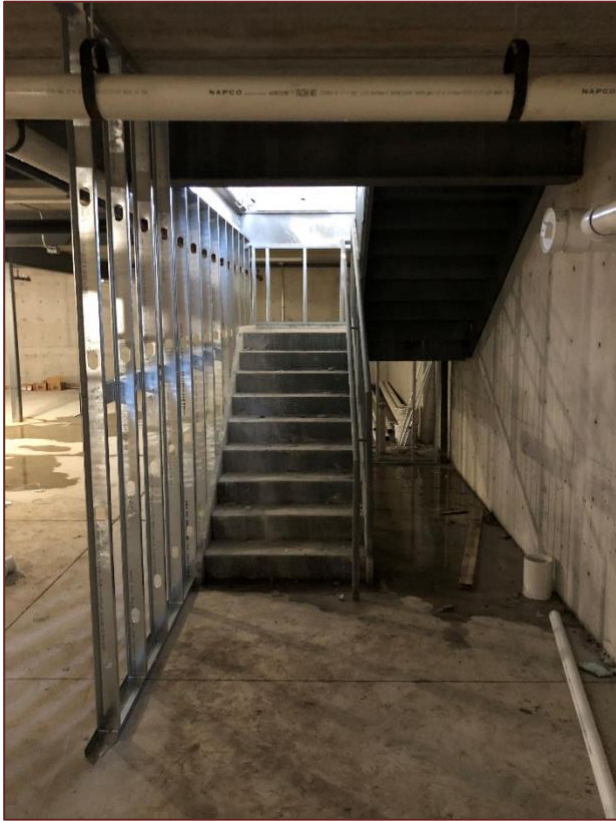

Basement door location.



Community Room.



Team meeting.

