



## The Township Center Project - 2020

---



SUBJECT: DAILY DIARY October 12, 2020

WEATHER: 60's degrees, overcast and rain in the afternoon.

WORK DAY = 87.

E. P. DOYLE: Graham on site today.

TALON: +1.

METAL MASTERS: +4.

HVAC: Units delivered.

STANTON: Don +2.

CALIBER: Larry +2.

MTZ: Ed on-site for meetings.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

### Activities Today:

- Talon = installing conduit on first floor and in basement.
- Stanton = continues working on plumbing in the basement and on 1<sup>st</sup> floor.
- Caliber = continues working on the first floor walls.
- Metal Masters = working on the roof.
- HVAC units delivered and placed on the roof.

### Activities Planned for Tuesday:

- Carpenters are finishing up.
- Electricians are finishing up.
- Plumbing work is finishing up.
- Bricks to be delivered.

### Critical Path:

- Masonry work.

### Pending Items:

- Get NICOR scheduled.

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

# The Township Center Project - 2020




The north and west elevations.



The roof.



# The Township Center Project - 2020

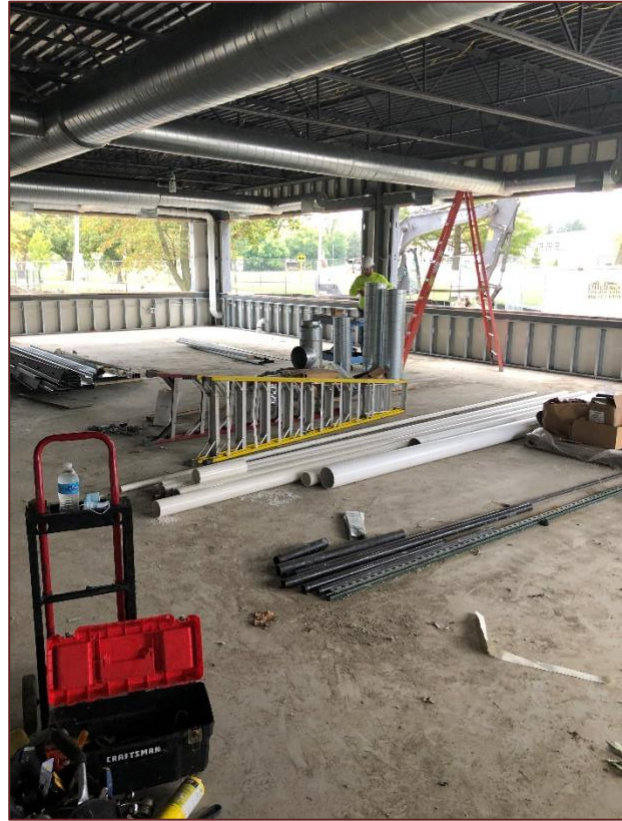

*The north elevation and the Community Room.*



*The basement.*
