



## The Township Center Project - 2020

---



SUBJECT: DAILY DIARY October 14, 2020

WEATHER: 60's degrees, variable.

WORK DAY = 89.

E. P. DOYLE: Graham on site today.

TALON: +1.

METAL MASTERS: +4.

ARCHON: +2.

STANTON: Don +2.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

### Activities Today:

- Talon = installing conduit on first floor and in basement.
- Stanton = continues working on plumbing in the basement and on 1<sup>st</sup> floor and the gas piping.
- Metal Masters = working on the roof.
- Archon worked on chlorination of the new water service and installation of the gas service. Village to inspect the chlorination process tomorrow.

### Activities Planned for Thursday:

- Roofers are finishing up.
- Electricians are finishing up.
- Plumbing work is finishing up.
- Bricks installation to begin.

### Critical Path:

- Masonry work to start on Thursday.


### Pending Items:

- Com Ed scheduled for November 9.
- Get NICOR scheduled.


Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

# The Township Center Project - 2020

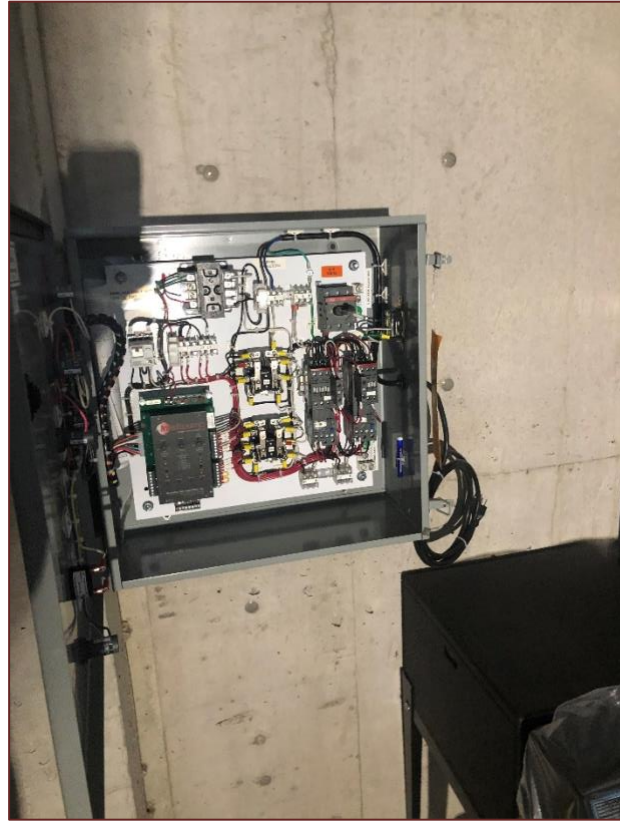

The new sump pump systems.

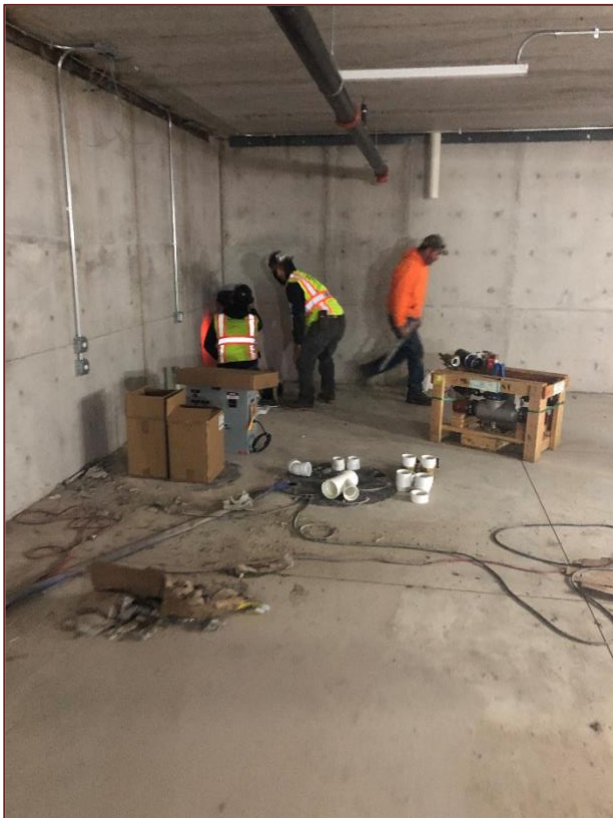

Working on the water service and the main hallway.

## The Township Center Project - 2020



Working on the gas service and testing the gas piping.
