



## The Township Center Project - 2020

---



SUBJECT: DAILY DIARY October 15, 2020

WEATHER: 50's degrees, variable.

WORK DAY = 90.

E. P. DOYLE: Graham on site today.

TALON: +2.

EBBEN: +5.

STANTON: Don +1.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

MTZ: Ed on-site

### Activities Today:

- Talon = installing conduit on first floor and in basement.
- Stanton = continues working on plumbing in the basement and on 1<sup>st</sup> floor and the gas piping.
- Ebben = brick layers begin work today.
- Ed Martinez on-site to coordinate with the brick layers.

### Activities Planned for Friday:

- Brick installations.
- Electricians are finishing up.
- Plumbing work is finishing up.

### Critical Path:

- Get NICOR Scheduled.

### Pending Items:


- Com Ed scheduled for November 9.

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.



The masons are on-site.

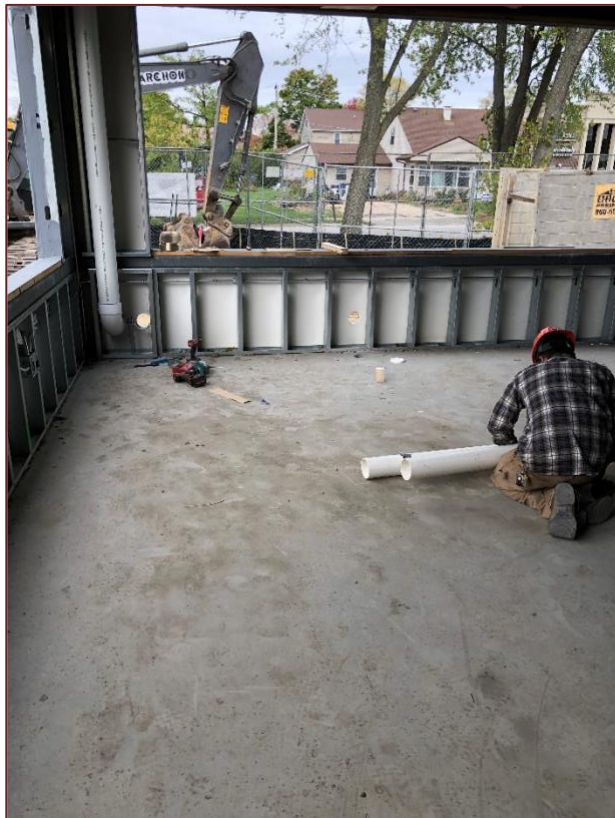

Work on first floor.



Work in the basement.
