



The Township Center Project - 2020



SUBJECT: DAILY DIARY October 16, 2020

WEATHER: 40's degrees, variable.

WORK DAY = 91.

E. P. DOYLE: Graham on site today. Russ on-site.

TALON: +2.

EBBEN: +5.

STANTON: Don +2.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

MTZ: Ed on-site

Activities Today:

- Talon = installing conduit on first floor.
- Stanton = continues working on plumbing in the basement.
- Ebben = brick layers working today.
- Ed Martinez and Russ on-site to coordinate with the brick layers.
- Plumbers passed their Village inspection today. Graham – I need copy of this paperwork.

Activities Planned for Monday:

- Brick installations.
- Electricians are finishing up.
- Plumbing work is finishing up.

Critical Path:

- Get NICOR Scheduled.

Pending Items:

- Com Ed scheduled for November 9.

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020




The bricklayers.



Electricians on first-floor.



Plumbers work in the basement.

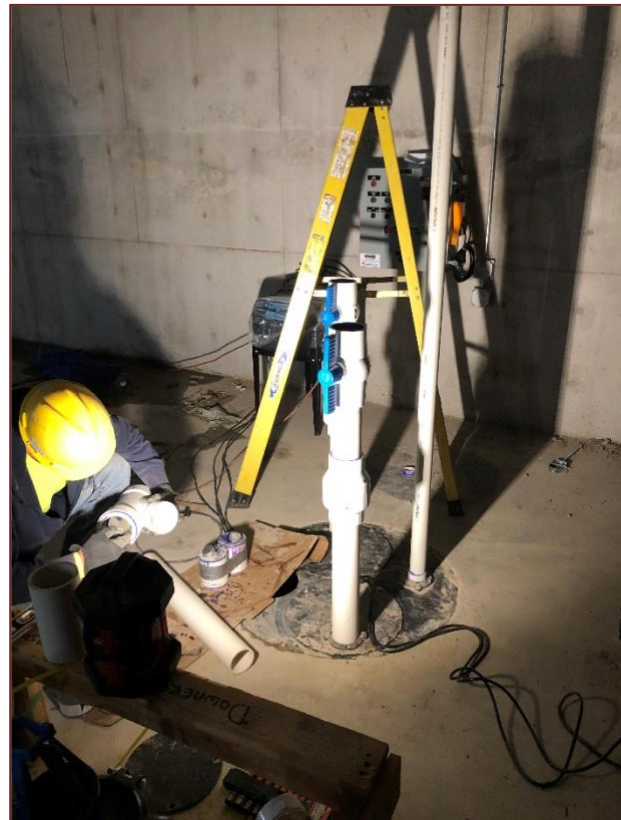

The Township Center Project - 2020



Brickwork today.



Brickwork today.
