



The Township Center Project - 2020



SUBJECT: DAILY DIARY October 23, 2020

WEATHER: 50's degrees. Rains today.

WORK DAY = TODAY = RAIN DAY = 94 + 0 = 94.

E. P. DOYLE: Graham on site today.

TALON: +2.

STANTON: +2.

EBBEN: +0.

MTZ: Ed on-site for team meeting.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today:

- Talon = Finishing installation of conduit on first floor.
- Ebben = Rained out.
- Plumbing Insulator wrapped the water pipes.
- Team Meeting – coordination of walk-in refrigeration units.

Activities Planned for Monday:

- Brick installations.
- Electricians are finishing up.
- Survey layout on Tuesday.

Critical Path:

- Get NICOR Scheduled.

Pending Items:

- Com Ed scheduled for November 9.
- Archon - Parking Lot Construction starts next week.

Please advise if there are questions or if I missed anything.


Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020



South Side.

The Work Room Refrig/Freezer Coord Meeting.

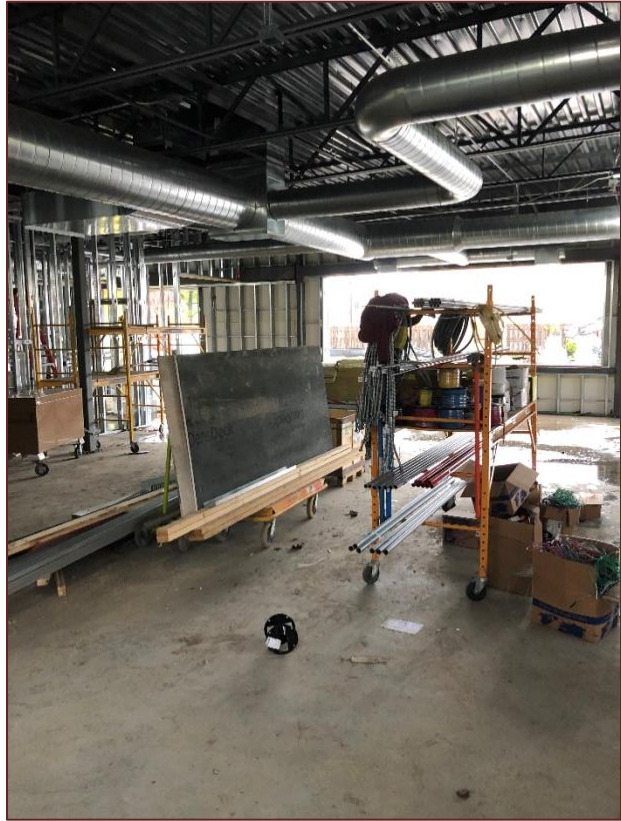

North Side.
