



The Township Center Project - 2020



SUBJECT: DAILY DIARY October 28, 2020

WEATHER: 30's and 40's and 50's degrees. sunny.

WORK DAY = TODAY = 96 + 1 = 97.

E. P. DOYLE: Graham on site today.

TALON: .

EBBEN: +9.

ARCHON: +6. And + 5 trucks.

FIRE ALARM: +1.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today:

- Ebben = Installing brickwork today.
- Archon begins excavation of the comp storage under the parking lot.

Activities Planned for Thursday:

- Brick installation completion?
- Electricians are finishing up.
- Archon to excavate the parking lot. More trucks might help production.

Critical Path:

- Get NICOR Scheduled.
- Get the windows scheduled.


Pending Items:

- Com Ed scheduled for November 9.

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020

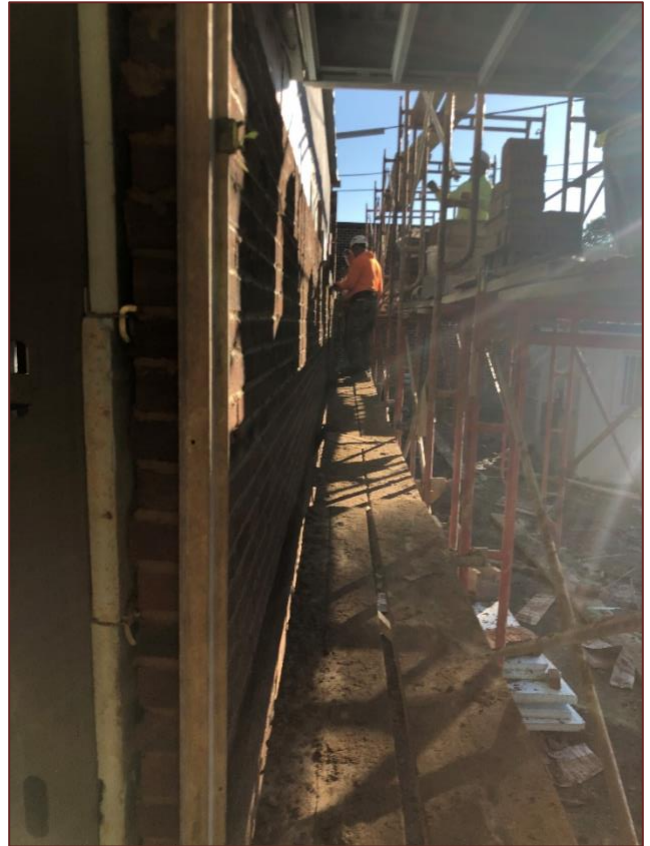

The brick work today.



The brick work today.

The Township Center Project - 2020



Excavation today under the parking lot for comp storage.



Excavation today under the parking lot for comp storage



Fabrics for the comp storage under the parking lot.



Wrapped water pipe.



Plumbing for the bathrooms.
