



The Township Center Project - 2020



SUBJECT: DAILY DIARY October 30, 2020

WEATHER: 30's degrees. And sunny.

WORK DAY = TODAY = 98 + 1 = 99.

E. P. DOYLE: Graham on site today.

TALON: .

ARCHON: +6. And + 10 trucks.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today:

- Archon continues excavation of the comp storage under the parking lot.

Activities Planned for Monday:

- Archon to excavate and construct the comp storage under the parking lot.
- Brick cleaners to be on-site.

Critical Path:

- Get NICOR Scheduled.

Pending Items:

- Com Ed scheduled for November 9.
- Windows are scheduled to be delivered the end of next week.

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020




The brick work is complete.




The brick work is complete.

The Township Center Project - 2020

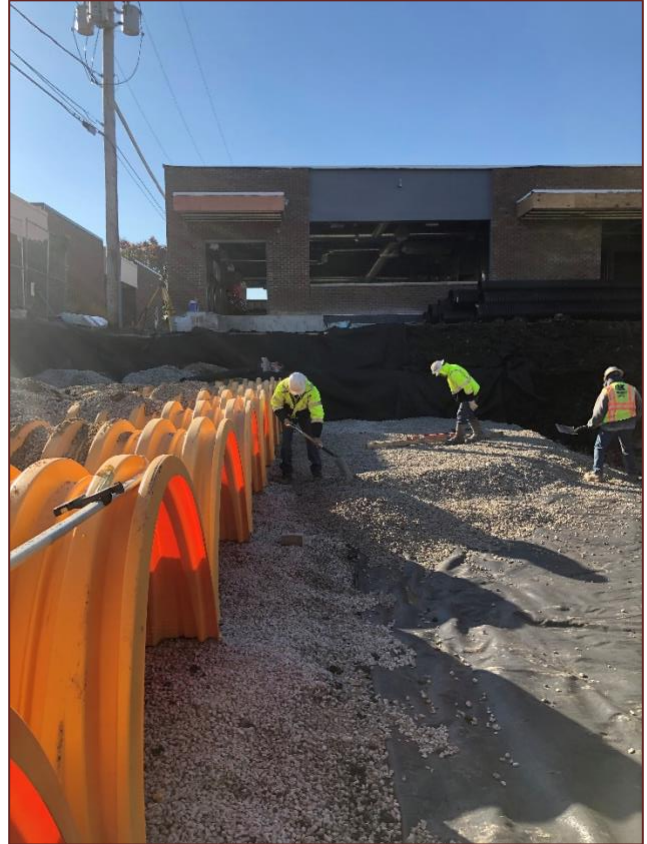

Excavation today and constructing the comp storage under the parking lot.

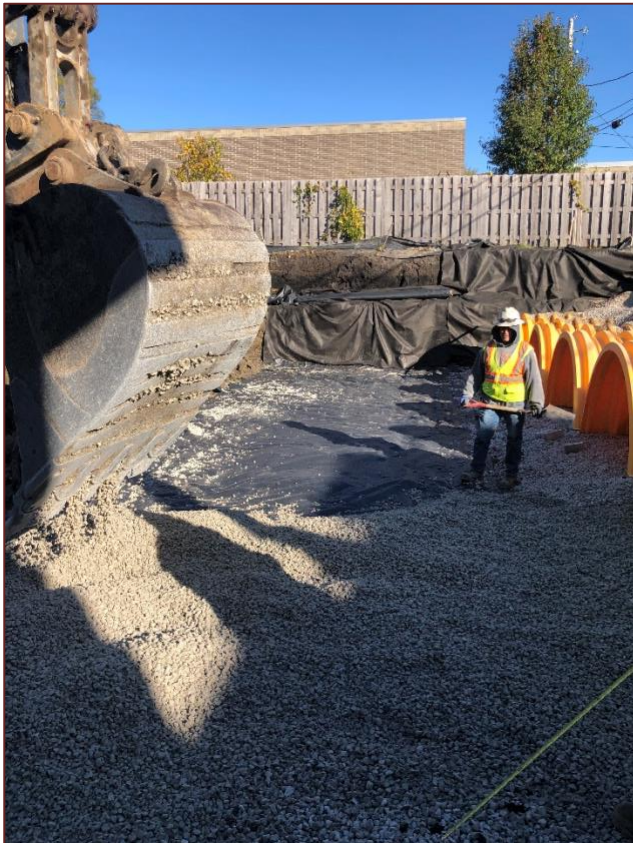

Excavation today and constructing the comp storage under the parking lot.
