



## The Township Center Project - 2020

---

SUBJECT: DAILY DIARY November 25, 2020

WEATHER: 30's degrees. Rain all day.

WORK DAY = TODAY = 115 + 1 = 116.

EP DOYLE: Graham and Ed on-site.

CALIBER: + 3.

WALKER: + 0.

TALON: + 1.

EIFIS: +0 .

PREMIUM [LCI CONCRETE] : +0.

COM ED: +0 .

STANTON: +1.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

### Activities Today :

- Caliber to continue working on drywall.
- Work on electrical in the kitchen.
- HVAC work in the basement.

### Activities Planning.

- Friday – OFF
- Monday – back at it.

### Critical Path:

- Get the Gas and electric into the building and start the heating system.


### Pending Items:

- Coordinate the new sanitary clean-out. EWP is executed. Installation planned for next week.
- Roll and vibrate the parking lot in preparation for bricks.
- Planning the topsoil schedule and coordinate with Mark.

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.


# The Township Center Project - 2020

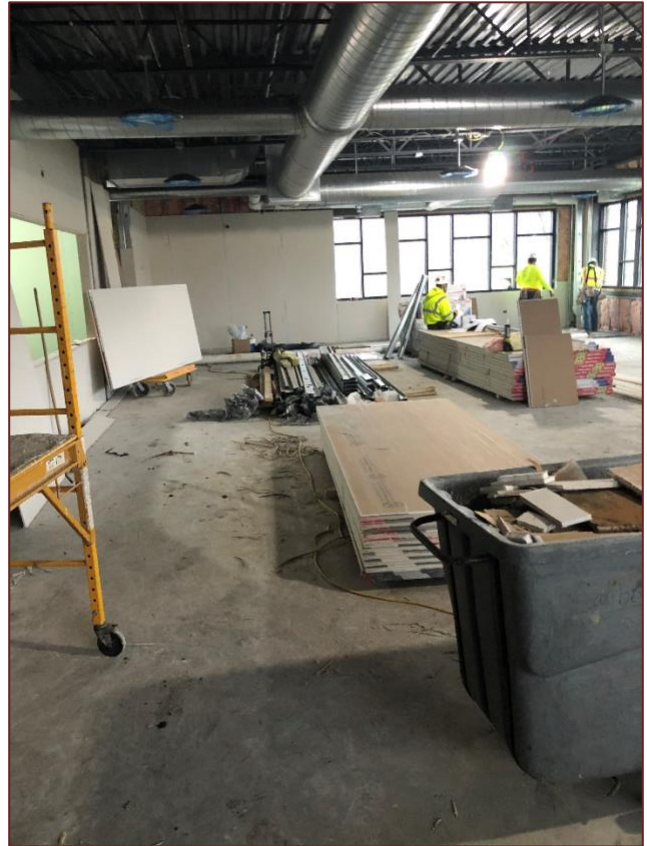

Drywall today.



Drywall today.

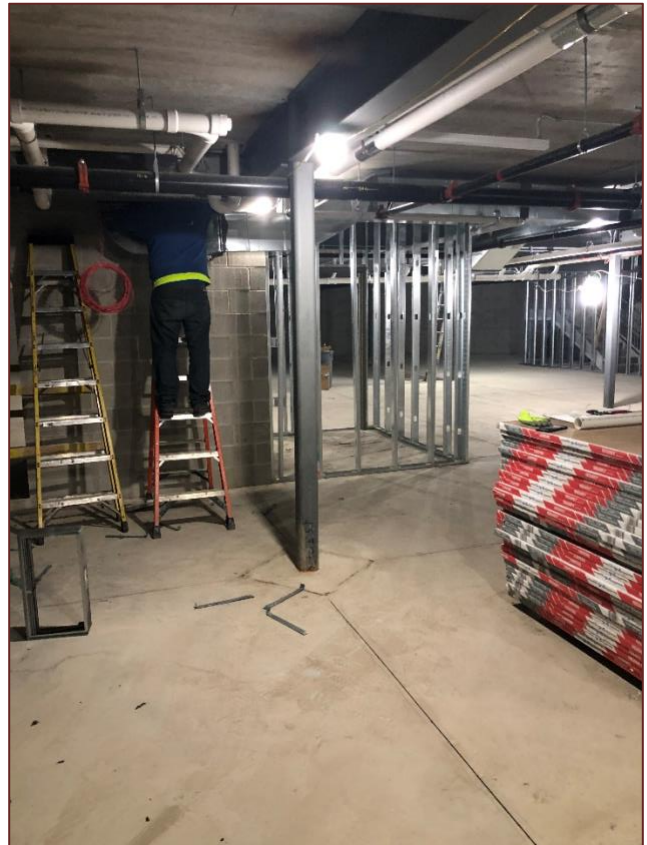

HVAC today.

# The Township Center Project - 2020



The west side.



The kitchen.
