



The Township Center Project - 2020



SUBJECT: DAILY DIARY November 30, 2020

WEATHER: 30's degrees. Cold all day.

WORK DAY = TODAY = 116 + 1 = 117.

EP DOYLE: Graham and Ed on-site.

CALIBER: + 3.

WALKER: + 2.

TALON: + 1.

EIFIS: +0 .

PREMIUM [LCI CONCRETE] : +0.

COM ED: +0 .

STANTON: +1.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today :

- Com Ed was on-site over the weekend, connecting power from the pole to our building.
- Caliber to continue working on drywall.
- Walker working on placing the topsoil.
- Work on electrical in the electrical closet.
- Plumbing connections in the basement.

Activities Planned for Tuesday.

- Work on Topsoil.
- Work on drywall.

Critical Path:

- **Get Com Ed to install our electrical meter. The building needs to be heated up.**

Pending Items:

- Install the new sanitary clean-out.
- Roll and vibrate the parking lot in preparation for bricks.
- Complete the topsoil placement.
- Complete installing the drywall.


Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020



Com Ed connected to the pole over the weekend.

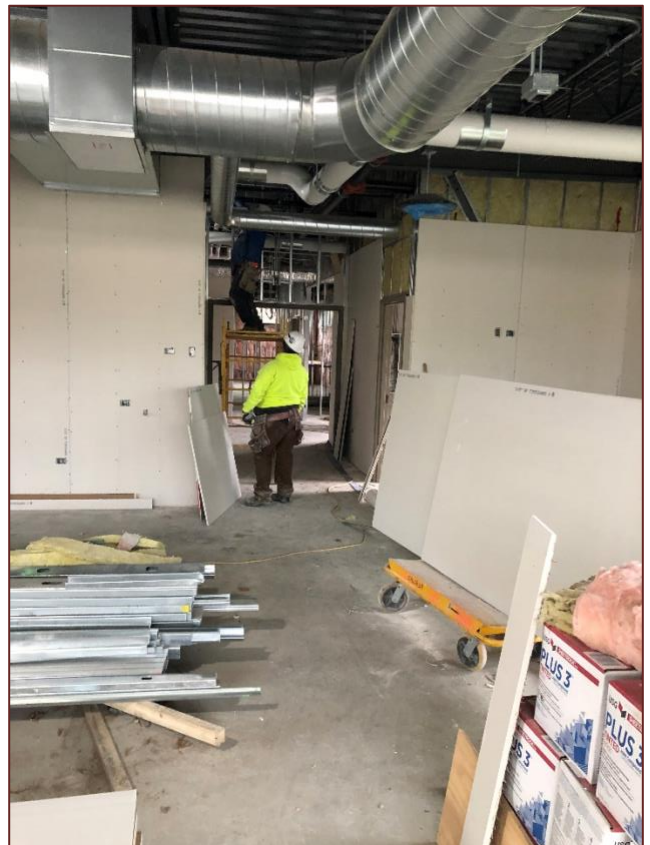

Drywall today.

The Township Center Project - 2020



Cleaning up the backyard.
