



The Township Center Project - 2020



SUBJECT: DAILY DIARY December 02, 2020

WEATHER: 30's degrees. Sunny.

WORK DAY = TODAY = 118 + 1 = 119.

EP DOYLE: Graham and Ed on-site.

CALIBER: + 3.

WALKER: + 3.

TALON: + 0.

J P PHILLIPS: +2 .

PREMIUM [LCI CONCRETE] : +0.

COM ED: +0 .

STANTON: +0.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today :

- Caliber to continue working on drywall.
- Walker working on placing the topsoil.
- Phillips working on EIFIS.

Activities Planned for Thursday.

- Work on Topsoil.
- Work on drywall.
- Thursday team meeting is in-person.

Critical Path:

- **Get Com Ed to install our electrical meter. The building needs to be heated up.**


Pending Items:

- Install the new sanitary clean-out.
- Roll and vibrate the parking lot in preparation for bricks.
- Complete the topsoil placement.
- Complete installing the drywall.

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020

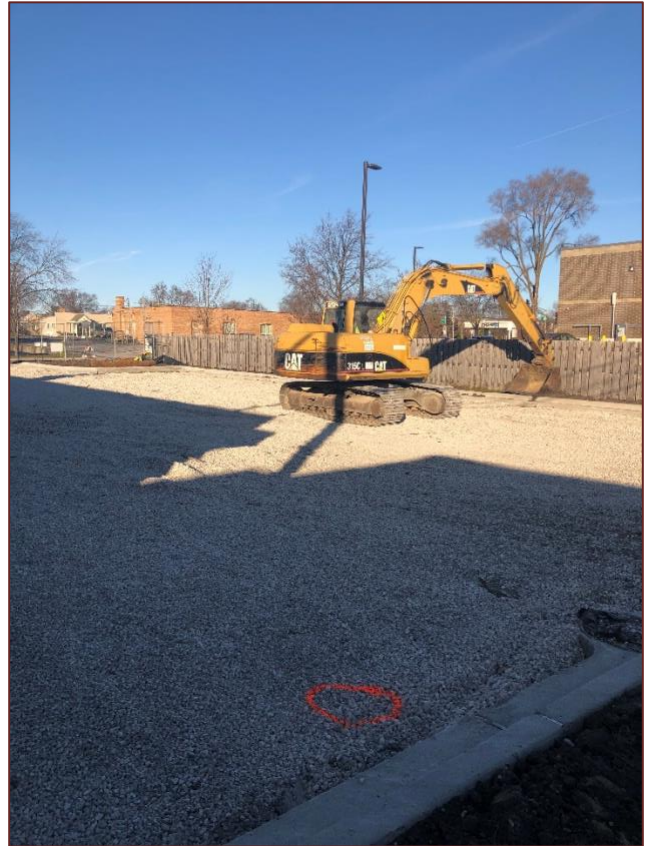

Working on the topsoil installation.



Drywall today.

The Township Center Project - 2020



EIFIS today.

