



## The Township Center Project - 2020

---



SUBJECT: DAILY DIARY December 03, 2020

WEATHER: 30's degrees. Sunny.

WORK DAY = TODAY = 119 + 1 = 120.

EP DOYLE: Graham and Russ on-site.

CALIBER: + 3.

WALKER: + 3.

TALON: + 1.

J P PHILLIPS: +2 .

PREMIUM [LCI CONCRETE] : +0.

COM ED: +0 .

STANTON: +0.

MTZ: Ed on site

ENGINEERING SOLUTIONS TEAM: Ed on-site.

### Activities Today :

- Caliber to continue working on drywall.
- Walker working on placing the topsoil. Parking Lot was compacted.
- Phillips working on EIFIS.
- Talon working in the electrical cabinet and downstairs.
- Project Team Meeting.

### Activities Planned for Friday.

- Work on Topsoil.
- Work on drywall.
- Install the sanitary sewer clean out
- Monday – Install the paver parking lot and back patio,

### Critical Path:

- **Get Com Ed to install our electrical meter. The building needs to be heated up.**



### Pending Items:

- Complete the topsoil placement.
- Complete installing the drywall.

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

# The Township Center Project - 2020

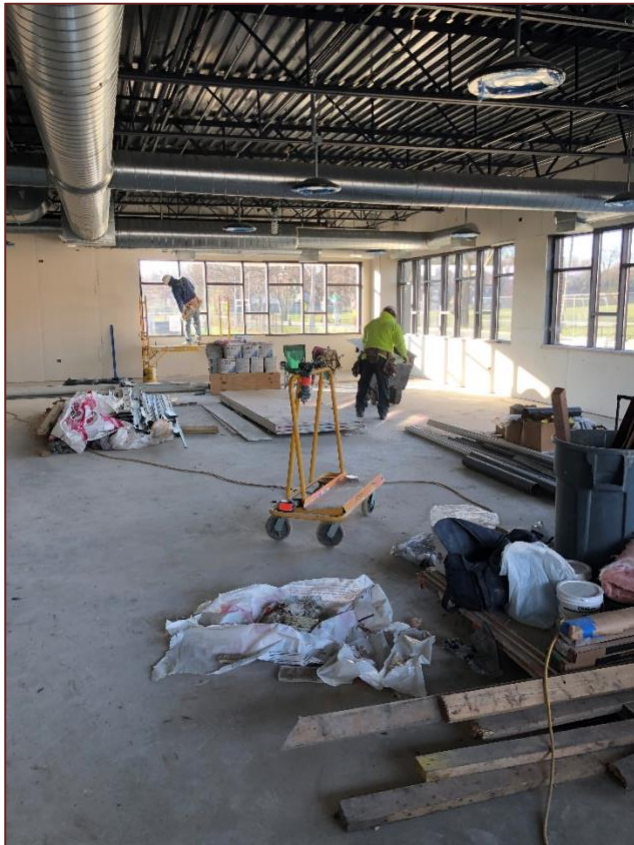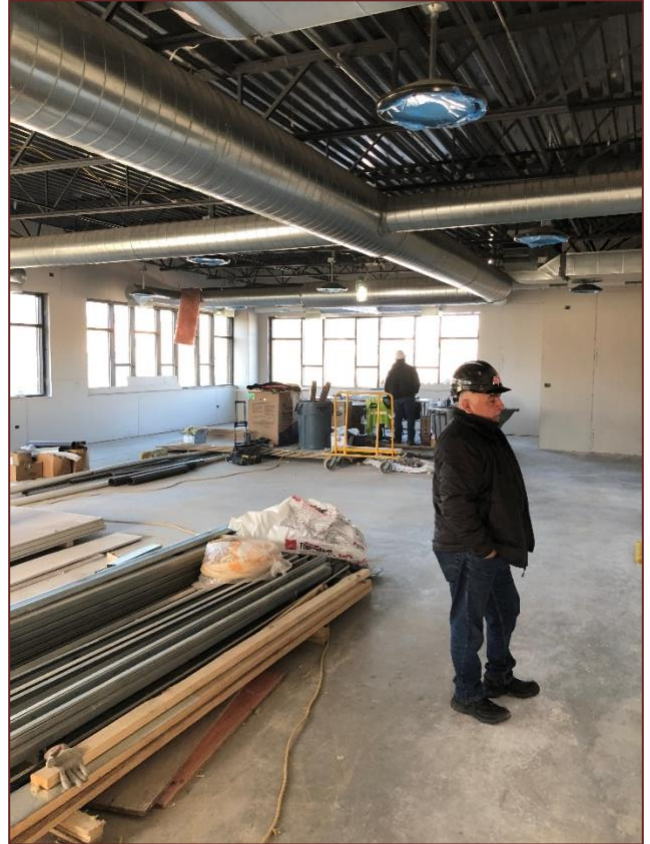

# The Township Center Project - 2020

