



The Township Center Project - 2020



SUBJECT: DAILY DIARY December 07, 2020

WEATHER: 30's degrees. Overcast.

WORK DAY = TODAY = 121 + 1 = 122.

EP DOYLE: Graham on-site.

CALIBER: + 3.

TALON: + 1.

J P PHILLIPS: +2 .

ARCHON: .

PREMIUM [LCI CONCRETE] : +0.

COM ED: + 2 crews .

STANTON: +0.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today :

- Caliber to continue working on drywall.
- Phillips working on EIFS.
- Talon working in the electrical cabinet and downstairs.
- Com Ed on-site to install the meter. Then to be back on-site to power-up the building.

Activities Planned for Tuesday.

- JB Mechanical to activate the RTU's.
- Work on drywall.
- Begin to install the paver parking lot and back patio.
- Concrete edge treatments and repairs to be begin.

Critical Path:

- **The building needs to be heated up.**

Pending Items:

- Complete installing the drywall.

Please advise if there are questions or if I missed anything.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020




Working on the EIFIS.



Com Ed meter is in.

The Township Center Project - 2020

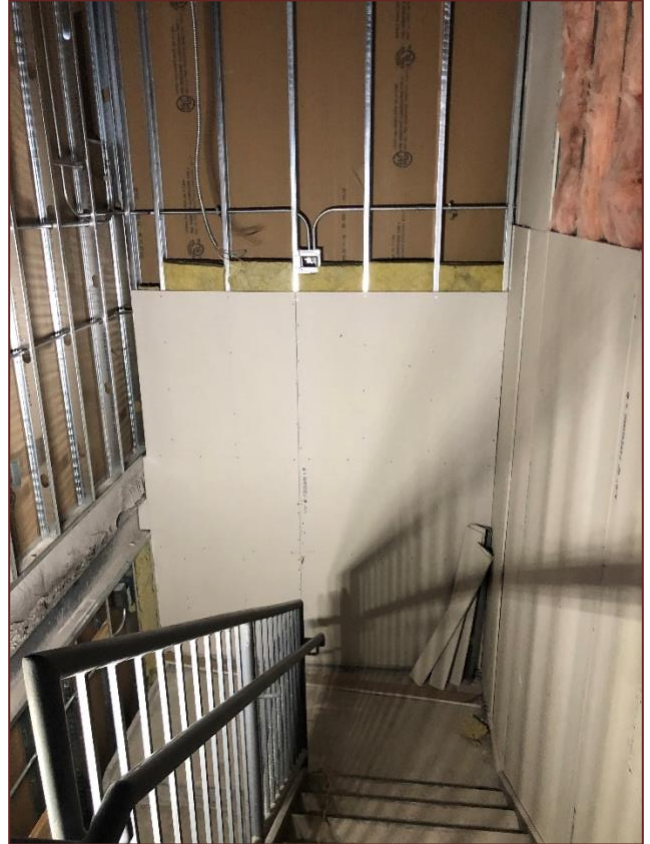

Working on the drywall.



EIFIS progress.
