



The Township Center Project - 2020



SUBJECT: DAILY DIARY December 18, 2020

WEATHER: 20's and 30's degrees. Partly cloudy.

WORK DAY = TODAY = 130 + 1 = 131.

EP DOYLE: Graham on-site.

CALIBER: +3.

LANDSCAPER: +2.

ADT: .

TALON: + 0.

PREMIUM [LCI CONCRETE] : +0.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today :

- Caliber to continue working on drywall and taping and sanding.
- Landscapers completed supply and installation of the river rock.
- Elevator is delivered to Schaumburg. We are on their install schedule.

Activities Planned for Monday.

- Work on drywall and taping and sanding.
- Concrete edge treatments and repairs scheduled for Tuesday.
- Continue working on electrical in the basement.
- Elevator progress.

Critical Path:


- Complete the taping and sanding.
- Complete the concrete repairs.

Pending Items:

- Install the elevator.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020

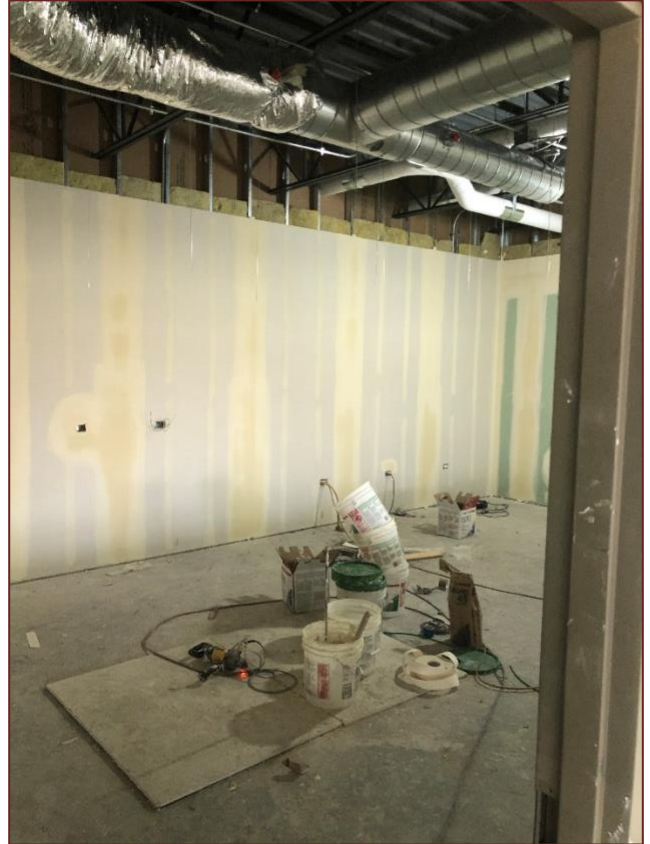

Work inside today.



The River Rock. Great energy dissipater.

The Township Center Project - 2020

