



The Township Center Project - 2020



SUBJECT: DAILY DIARY December 21, 2020

WEATHER: 30's and 40's degrees. Partly cloudy.

WORK DAY = TODAY = 131 + 1 = 132.

EP DOYLE: .

CALIBER: +2.

EIFIS: +1.

TALON: + 0.

PREMIUM [LCI CONCRETE] : +0.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today :

- Caliber to continue working on drywall and taping and sanding.
- EIFIS above the middle window is corrected.
- Elevator is delivered to Schaumburg. We are on their install schedule.

Activities Planned for Tuesday.

- Work on drywall and taping and sanding.
- Concrete edge treatments and repairs scheduled for Tuesday.
- Continue working on electrical in the basement.
- Elevator progress.

Critical Path:

- **Complete the taping and sanding.**
- **Complete the concrete repairs.**

Pending Items:


- Install the elevator.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020



Work today.

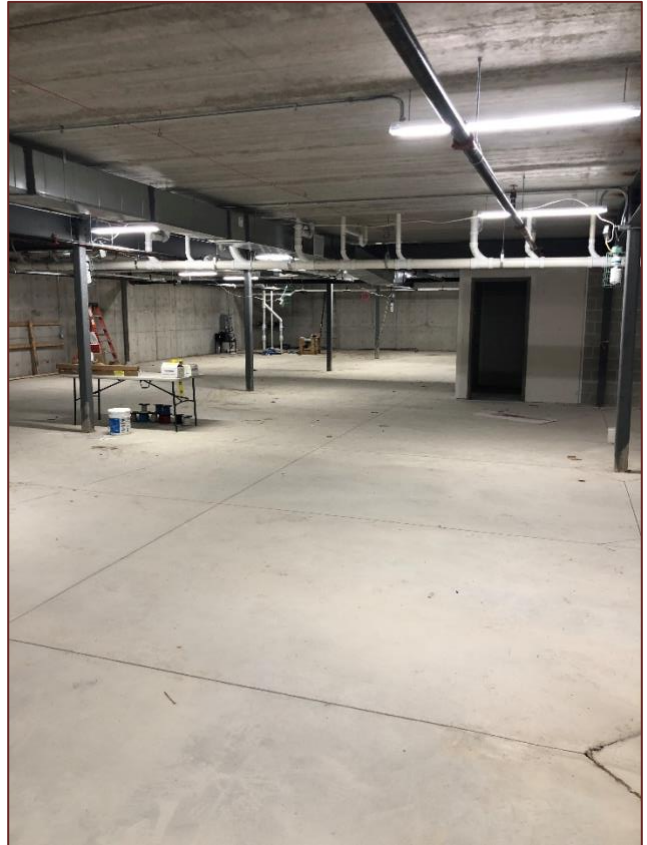

The Township Center Project - 2020

