



The Township Center Project - 2020

SUBJECT: DAILY DIARY December 28, 2020

WEATHER: 20's degrees. Mostly sunny.

WORK DAY = TODAY = $134 + 1 = 135$.

EP DOYLE: Graham.

CALIBER: +3.

TALON: + 0.

PREMIUM [LCI CONCRETE] : +1.

J P PHILLIPS: +1.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today :

- Caliber working on completion of drywall sanding.
- Phillips removes the scaffolding.
- Premium strips and removes the forms.

Activities Planned for Tuesday.

- Complete the drywall sanding.
- Remove the construction fence.

Critical Path:


- **Deliver and Install the Elevator.**

Pending Items:

- Repair the Kitchen Floor.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020

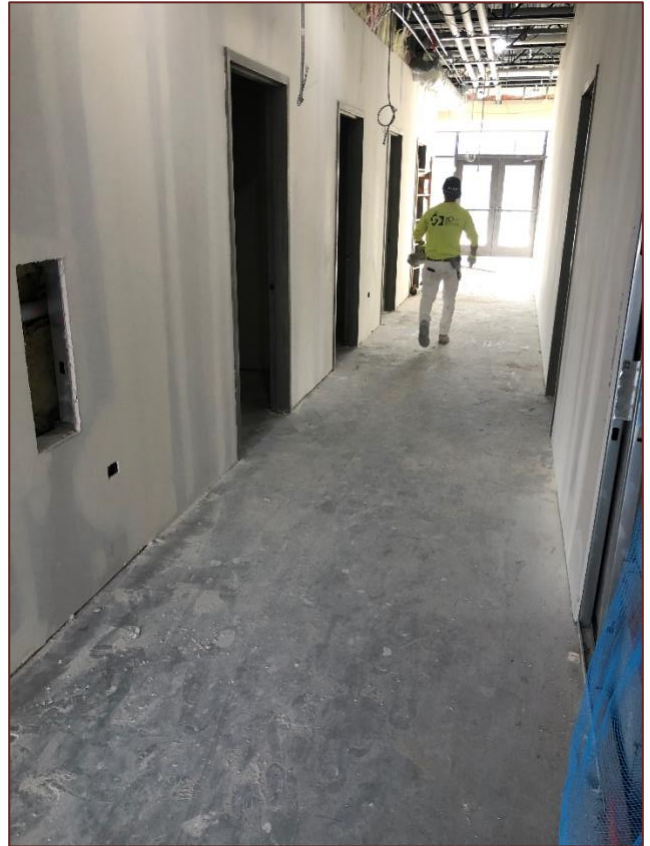

Finish Sanding.



Finish Sanding.



Basement Floor Drains.



Kitchen Floor in need of repairs.
