



The Township Center Project - 2020

SUBJECT: DAILY DIARY December 29, 2020

WEATHER: 20's degrees. Overcast.

WORK DAY = TODAY = 135 + 1 = 136.

EP DOYLE: Graham.

CALIBER: +3.

TALON: + 0.

PREMIUM [LCI CONCRETE] : +0.

CARDINAL: +1.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today :

- Caliber working on completion of drywall sanding in the basement.
- Paint the hallway.
- Remove the construction fence.
- Install the storefront doors.

Activities Planned for Wednesday.

- Complete the drywall sanding.
- Work on storefront doors.
- Painting.
- Repair the kitchen floor.

Critical Path:

- **Deliver and Install the Elevator.**

Pending Items:


- Repair the Kitchen Floor.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020



Painting of the hallway.

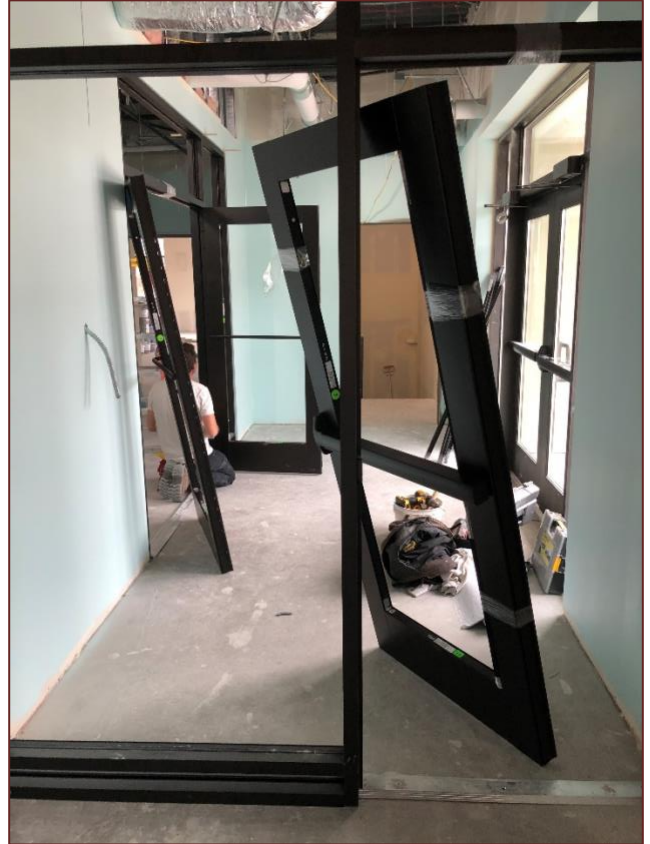

Storefront doors are being installed.



Construction fences are removed.
