



## The Township Center Project - 2020

---

SUBJECT: DAILY DIARY: January 4, 2021

WEATHER: 20's degrees. Overcast and foggy.

WORK DAY = TODAY = 137 + 1 [Dec 31] + 1 [today] = 139.

EP DOYLE: Graham.

CALIBER: +2.

TALON: +0.

JB MECH : +3.

ACTION FENCE: +2.

PAINTER: +1.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

### Activities Today :

- Complete the Trash Bin.
- Finishing the drop ceiling.
- Painting.
- Continue the insulation and duct details.

### Activities Planned for Tuesday.

- Painting.
- Deliver the elevator.
- Repair the kitchen floor.

### Critical Path:

- **Install the Elevator.**

### Pending Items:


- 

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

# The Township Center Project - 2020



Cleaning up the Township Room.

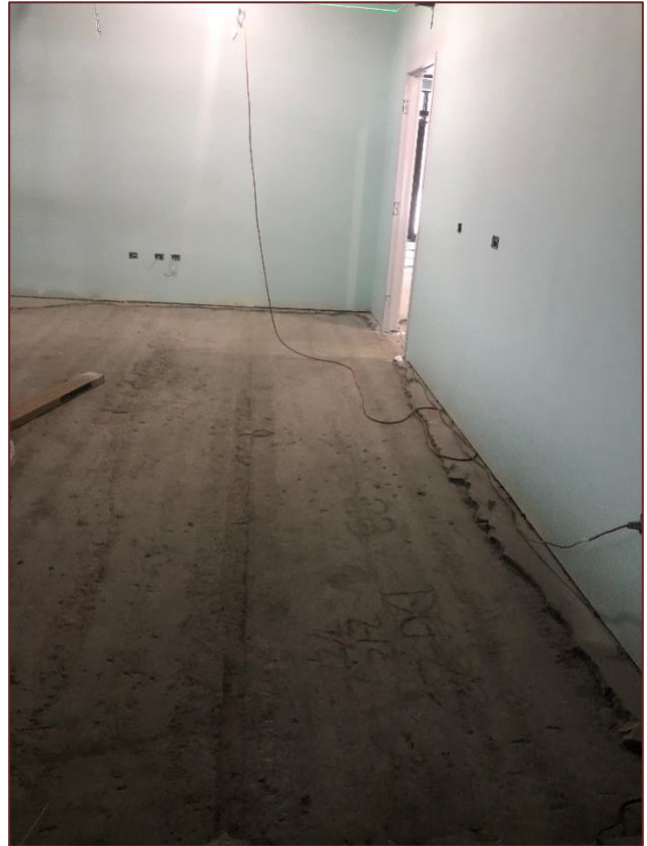

Kitchen floor is now being repaired.



Cleaning the basement.



Setting the ceiling grid in the hallway.



# The Township Center Project - 2020



Fencing the Trash Corral.



Painting in the Work Room.
