



The Township Center Project - 2020

SUBJECT: DAILY DIARY: January 7, 2021

WEATHER: 30's degrees. Overcast.

WORK DAY = TODAY = 141 + 1 = 142.

EP DOYLE: Graham.

CALIBER: +2.

NELSON FIRE: +1.

CARDINAL GLASS: +0.

TALON: +0.

PAINTER: +1.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today :

- Painted ceilings in the Food Pantry.
- Connect the Fire Suppression Systems.
- Install the VCT paneling in the Kitchen.
- Graham worked on contacting AT&T for the internet connection to the elevator. Better contact information is necessary.
- Project Team Meeting.

Activities Planned for Friday.

- Painting the ceilings
- Kitchen walls.
- AT&T coordination.
- Village inspection.
- Begin installation of the elevator.

Critical Path:

- **Install the Elevator.**

Pending Items:


- Repair of the kitchen floor scheduled for the 17th.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020



Connecting the Fire Safety System.

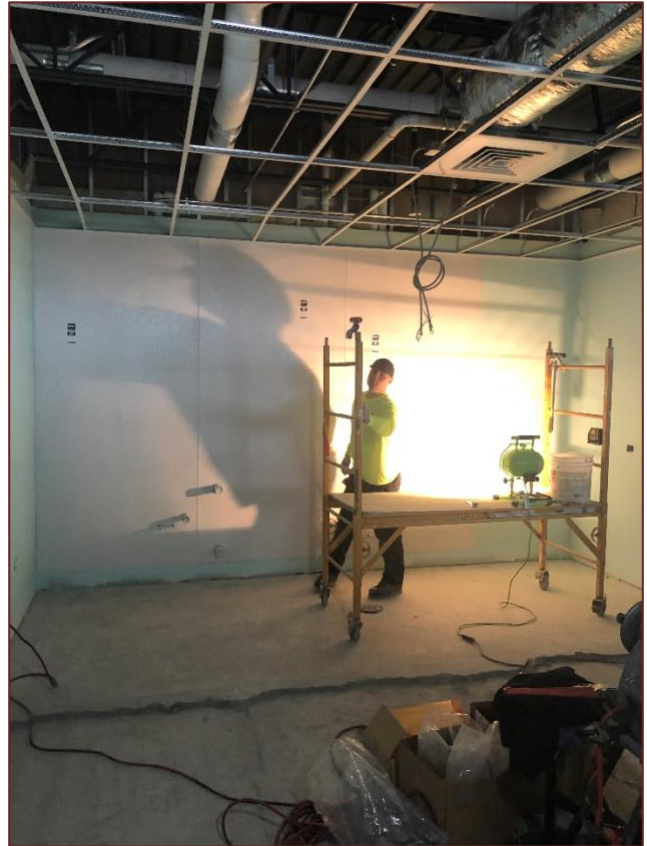

Installing VCT in the Kitchen.



Work in the bathrooms.



Painting the ceiling in the Food Pantry.



Painting the ceiling in the Food Pantry.
