



## The Township Center Project - 2020

---



SUBJECT: DAILY DIARY: January 8, 2021

WEATHER: 30's degrees. Overcast.

WORK DAY = TODAY = 142 + 1 = 143.

EP DOYLE: Graham.

CALIBER: +2.

SCHINDLER: +2.

NELSON FIRE: +1.

JB MECH: +1.

TALON: +2.

PAINTER: +1.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

### Activities Today :

- Begin installation of the elevator.
- Painted ceilings in the Food Pantry.
- Connect the Fire Suppression Systems. Village Fire Department came out to inspect. Inspection passed. A couple comments were made about the elevator.
- Install the FRP paneling in the Kitchen.
- Electrician work on ceiling lighting and trim.
- Graham scheduled AT&T for next week.

### Activities Planned for Monday.

- Painting the ceilings
- Kitchen walls.
- Continue installation of the elevator.
- Electrician to continue ceiling lighting.

### Critical Path:



- **Complete the Elevator installation.**

### Pending Items:

- Repair of the kitchen floor scheduled for the 17<sup>th</sup>.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

# The Township Center Project - 2020

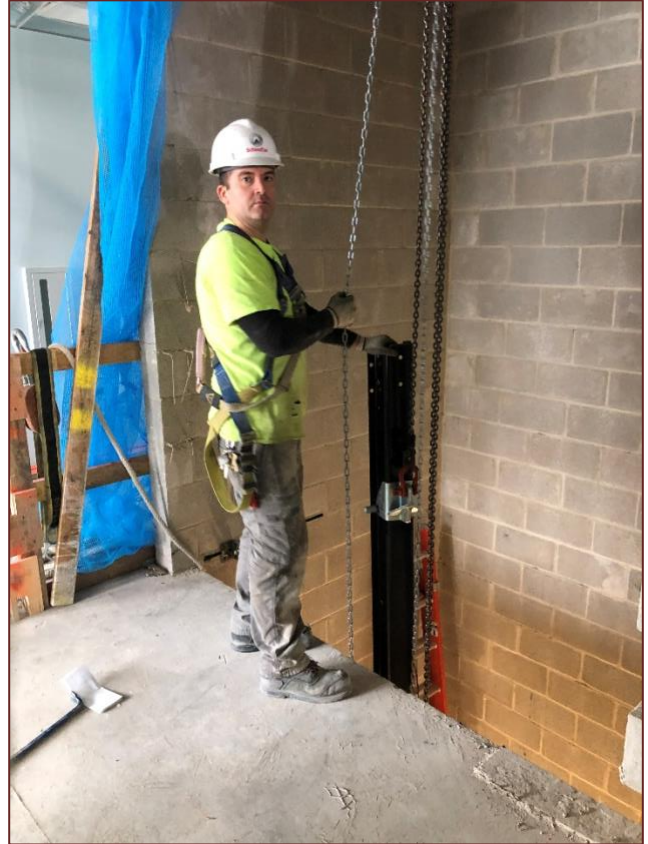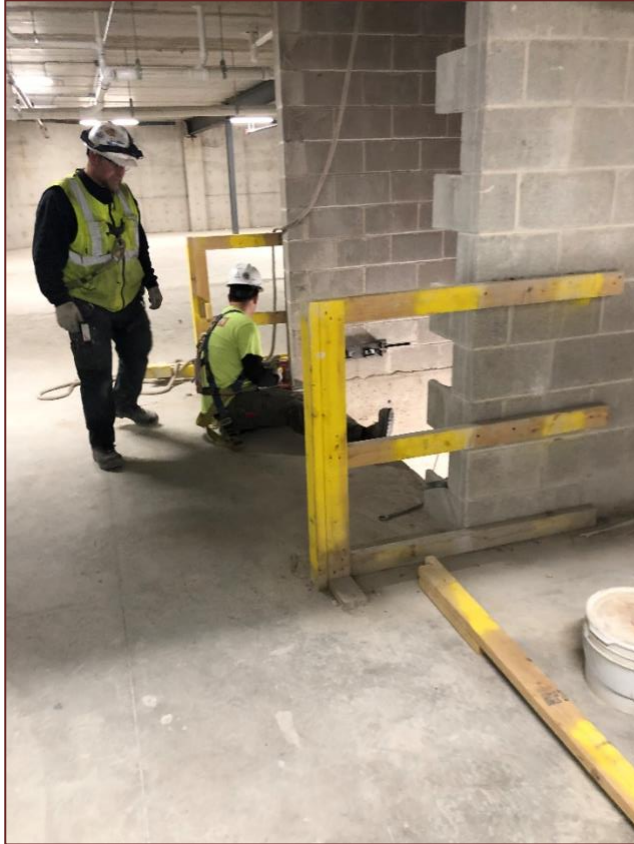


Working on the elevator.



The Hallway.



The Township Room.

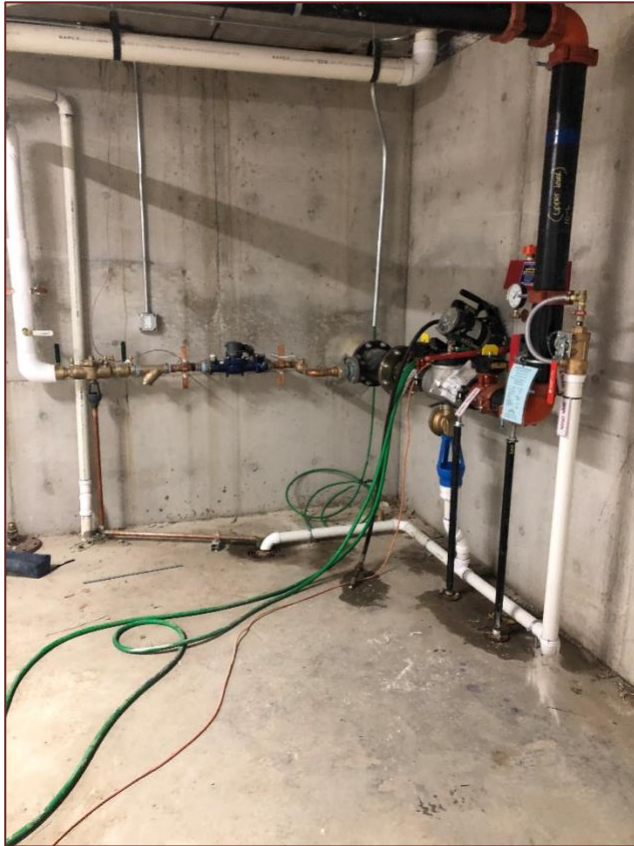

Fire suppression system.



Hallway units.



The Food Pantry.
