



## The Township Center Project - 2020

---

SUBJECT: DAILY DIARY: January 11, 2021

WEATHER: 20's degrees. Overcast.

WORK DAY = TODAY = 143 + 1 = 144.

EP DOYLE: Graham.

CALIBER: +0.

SCHINDLER: +2.

JB MECH: +0.

TALON: +1.

PAINTER: +2.

STANTON: +1.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

### Activities Today :

- Continue installation of the elevator.
- Painting final coats in the Food Pantry and in the stairwells.
- Electrician work on ceiling lighting and trim.
- Plumber worked on the hot water heater.

### Activities Planned for Tuesday.

- Continue painting
- Continue installing the elevator.
- Electrician to continue ceiling lighting.
- Continue to work on plumbing details.

### Critical Path:


- **Complete the Elevator installation.**

### Pending Items:


- Repair of the kitchen floor scheduled for the 17<sup>th</sup>.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

# The Township Center Project - 2020

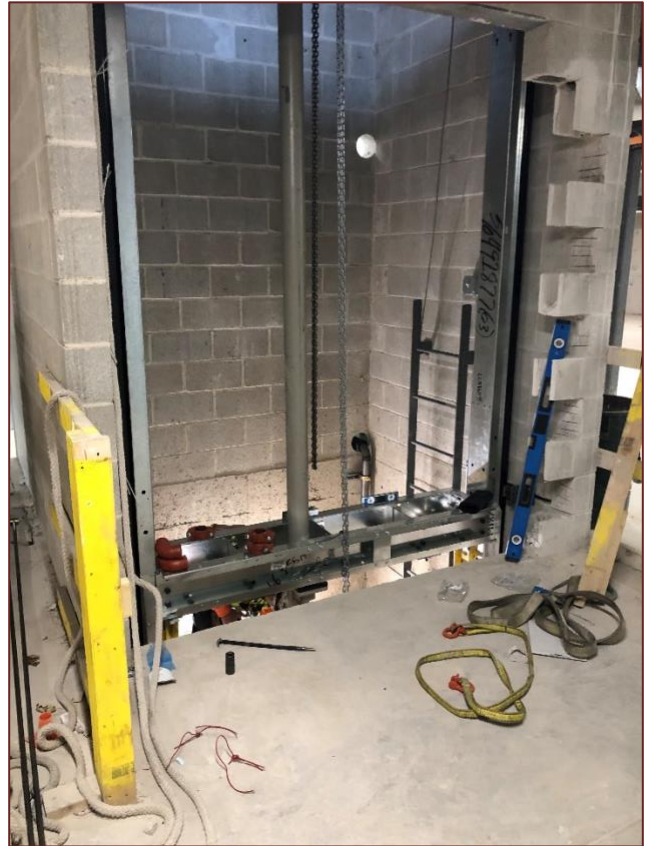

Working on the elevator.

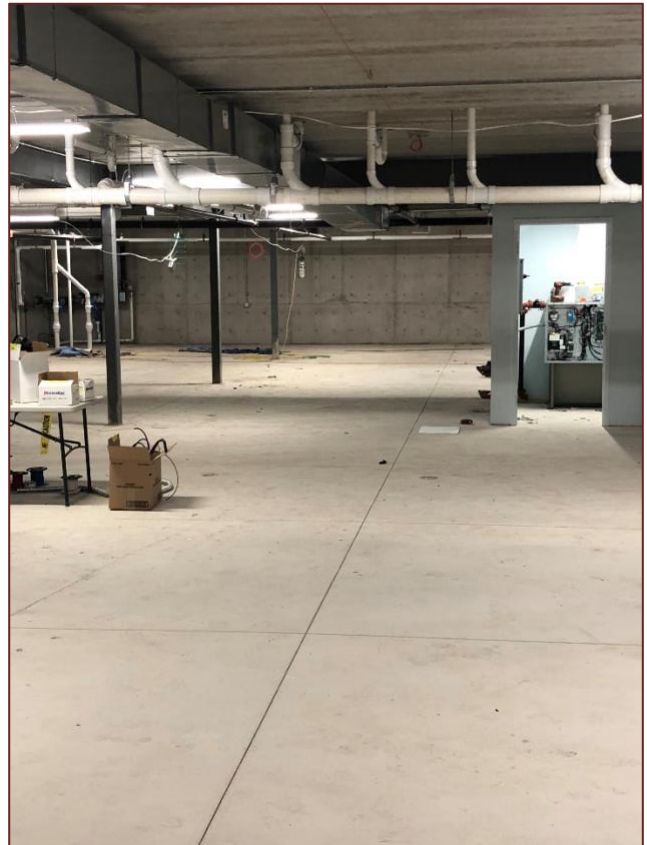


Working on the elevator.

# The Township Center Project - 2020



The Kitchen.

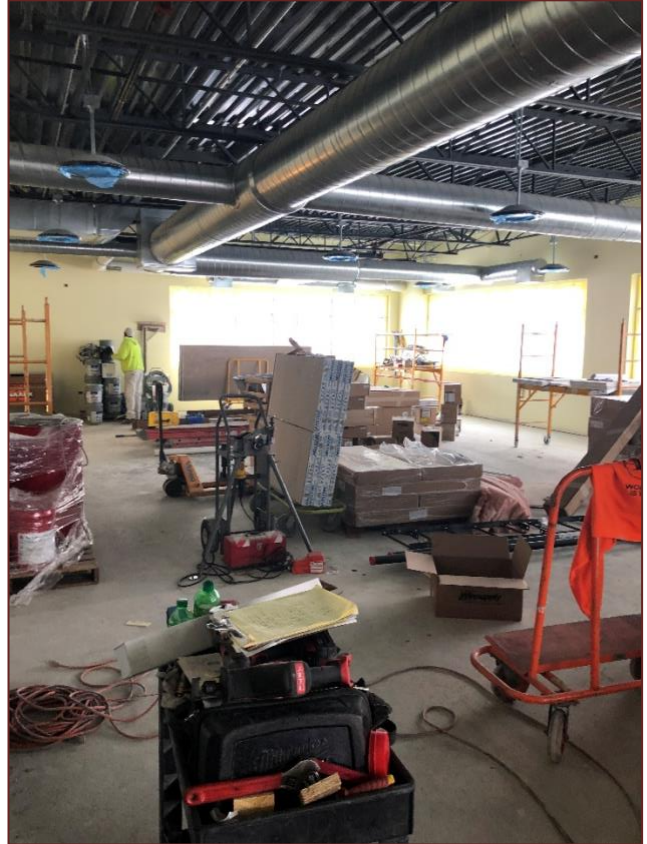

The Township Room.



The Food Pantry.
