



## The Township Center Project - 2020

---

SUBJECT: DAILY DIARY: January 12, 2021

WEATHER: 30's degrees. Sunny.

WORK DAY = TODAY = 144 + 1 = 145.

EP DOYLE: Graham.

CALIBER: +0.

SCHINDLER: +2.

JB MECH: +0.

TALON: +1.

PAINTER: +2.

STANTON: +1.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

### Activities Today :

- Continue installation of the elevator.
- Painting final coats in the Food Pantry and in the stairwells.
- Electrician work on ceiling lighting and trim.
- Plumber worked on the bathrooms.

### Activities Planned for Wednesday.

- Continue painting
- Continue installing the elevator.
- Electrician to continue ceiling lighting.
- Continue to work on plumbing details.
- Team ceiling inspection. Village inspection scheduled for Thursday.


### Critical Path:

- **Complete the Elevator installation.**


### Pending Items:

- Repair of the kitchen floor scheduled for the 17<sup>th</sup>.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

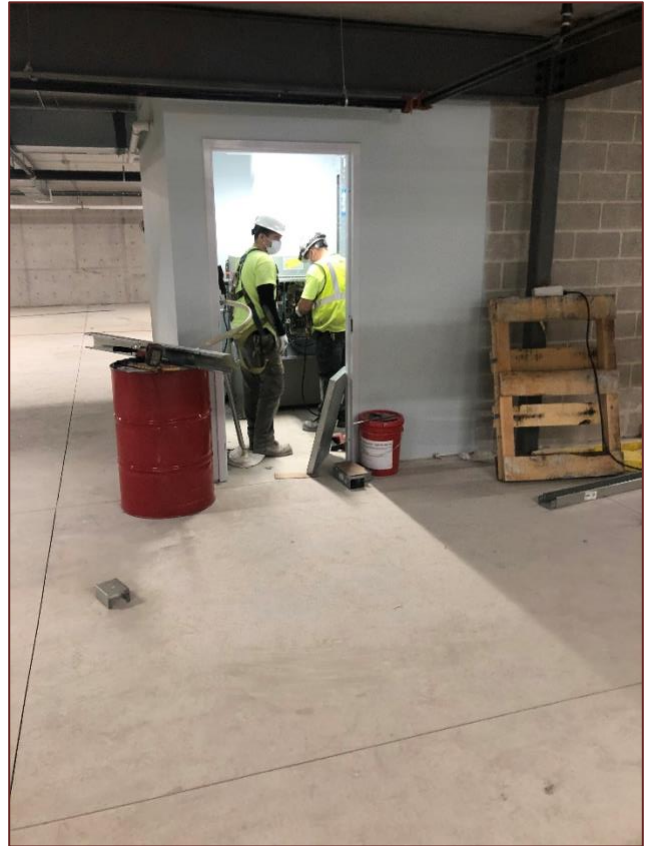


Working on the elevator.

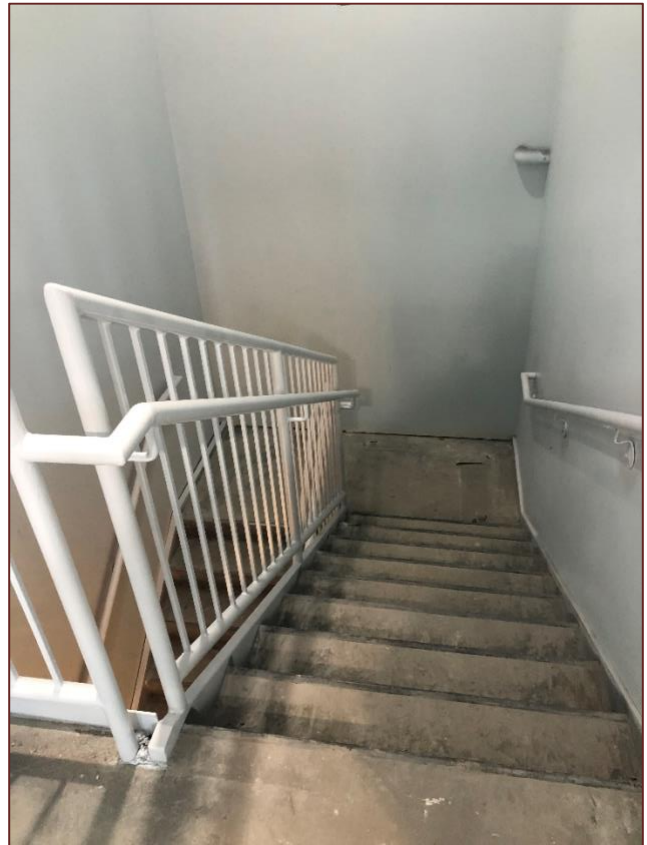

Working in the stairwells.

# The Township Center Project - 2020

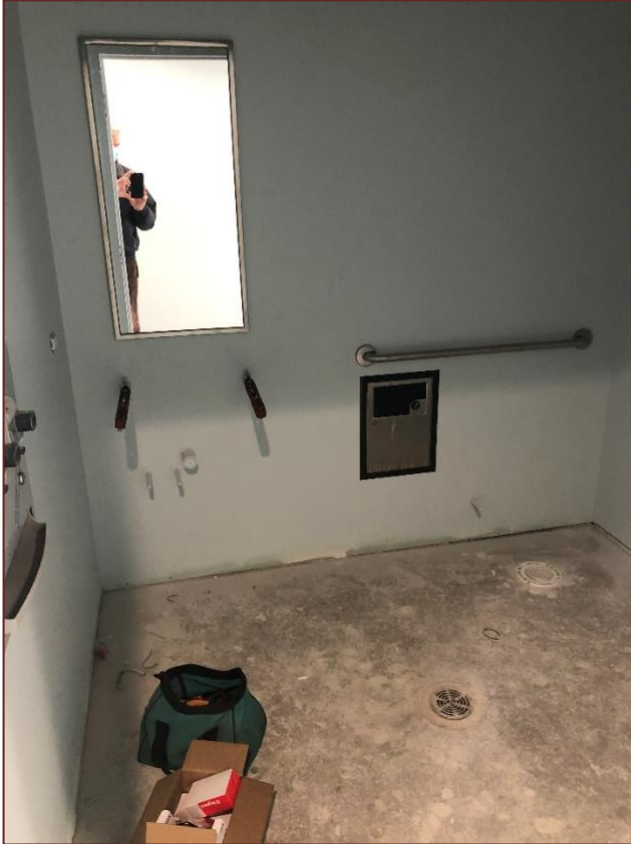

The Bathrooms.



The Township Room.



The Food Pantry.
