



The Township Center Project - 2020

SUBJECT: DAILY DIARY: January 18, 2021

WEATHER: 20's degrees. Overcast and windy and cold. All work was inside today.

WORK DAY = TODAY = 148 + 1 = 149.

EP DOYLE: Graham.

CALIBER: +1.

SCHINDLER: +2.

CROCK RIVER FLOORING: +2.

TALON: +2.

PAINTER: +0.

STANTON: +0.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today :

- Continue installation of the elevator.
- Electrician work on ceiling lighting and trim.
- Kitchen floor was repaired.
- Installed ceiling tiles.

Activities Planned for Monday.

- Clean and begin painting the Township Room.
- Complete installation of the elevator.
- Electrician to continue ceiling lighting.
- Continue to work on plumbing details.
- Begin the Floor Tiling.

Critical Path:

- **Complete the Elevator installation.**
- **Paint the Township Room.**

Pending Items:

- Install the Outside Lights.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020




Working on the elevator.



Repairing the Kitchen Floor.

The Township Center Project - 2020

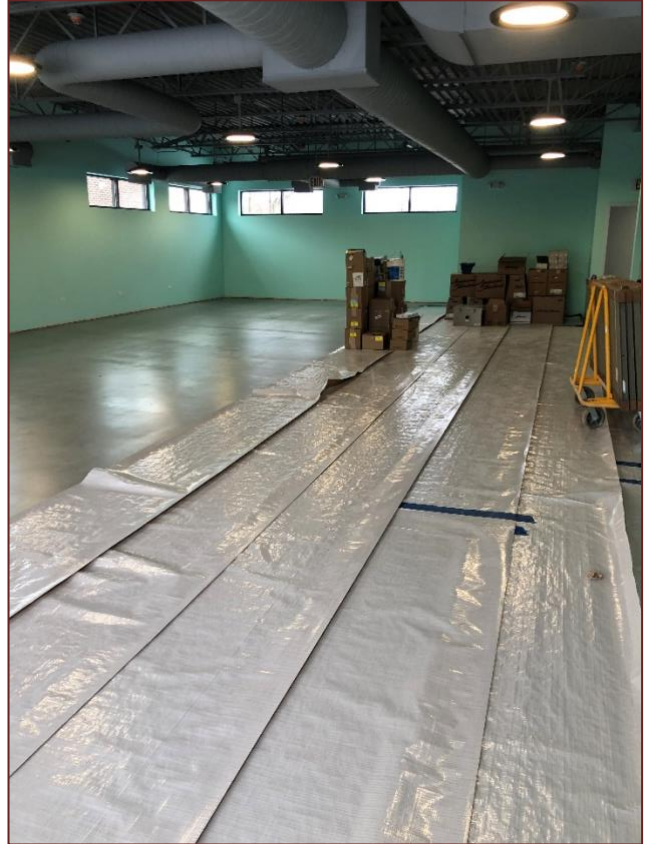

The Township Room and the Food Pantry.



The Hallway and the Drinking Fountains.
