



The Township Center Project - 2020



SUBJECT: DAILY DIARY: January 22, 2021

WEATHER: 10's degrees. Sunny and cold. All work was inside today.

WORK DAY = TODAY = 152 + 1 = 153.

EP DOYLE: Graham and Russ

CALIBER: +1.

SCHINDLER: +0.

ROCK RIVER FLOORING: +0.

TALON: +0.

PAINTER: + 1.

STANTON: +1.

EBBEN: +0.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

MTZ: Ed Martinez on-site.

Activities Today :

- Project Team Meeting.
- Begin to install the toilets.
- Continue tiling the first floor.
- Hanging Doors.
- Paint the Township Room.

Activities Planned for Monday.

- Team meeting at 9:00.
- Continue painting the Township Room.
- Continue to work on plumbing details.
- Continue the Floor Tiling. / Continue hanging doors.

Critical Path:

- **Paint the Township Room.**

Pending Items:

- Inspections and Commissioning scheduled for February 1.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.




The kitchen.



The Hallway.



The Bathroom.

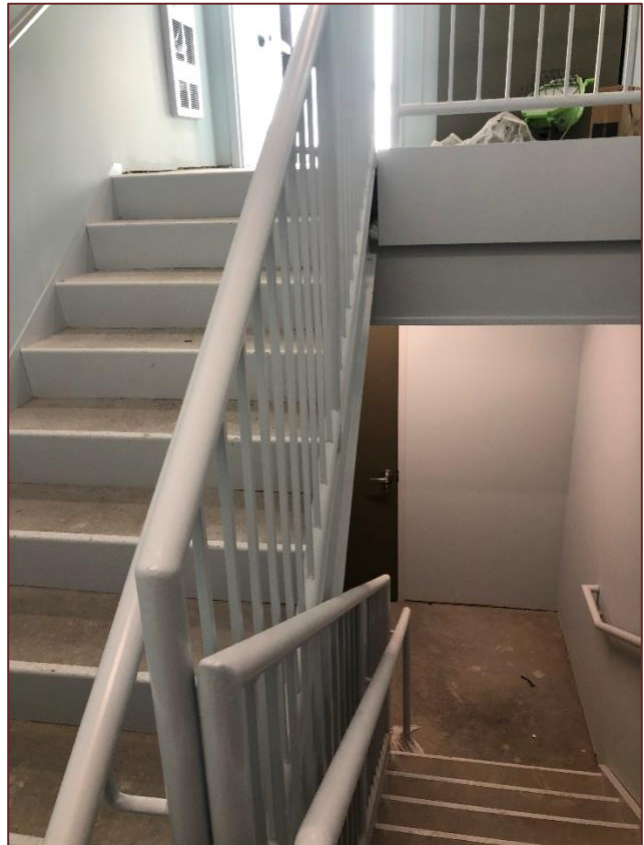

The Stairs.

The Township Center Project - 2020



The Food Pantry.



The Township Room.
