



## The Township Center Project - 2020

---

SUBJECT: DAILY DIARY: January 25, 2021

WEATHER: 20's degrees. Overcast. All work was inside today.

WORK DAY = TODAY = 153 + 1 = 154.

EP DOYLE: Graham and Russ

CALIBER: +1.

SCHINDLER: +1.

WEBSTER McGRATH: +1.

TALON: +1.

PAINTER: + 1.

STANTON: +1.

CLEANERS: +2.

GATOR CHEF: +4

ENGINEERING SOLUTIONS TEAM: Ed on-site.

### Activities Today :

- Complete the install of toilets.
- Hanging Doors.
- Paint the Township Room.
- Installation of Kitchen Equipment.
- As-built site survey.
- Program the elevator.
- Begin cleaning in the basement.

### Activities Planned for Tuesday.

- Continue all Final Detailing Work.

### Critical Path:

- Complete the RDA Document for Mark.

### Pending Items:

- Inspections and Commissioning scheduled for February 1.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.



Work in the kitchen.




The Bathroom.



Working on the refrigeration units.

# The Township Center Project - 2020

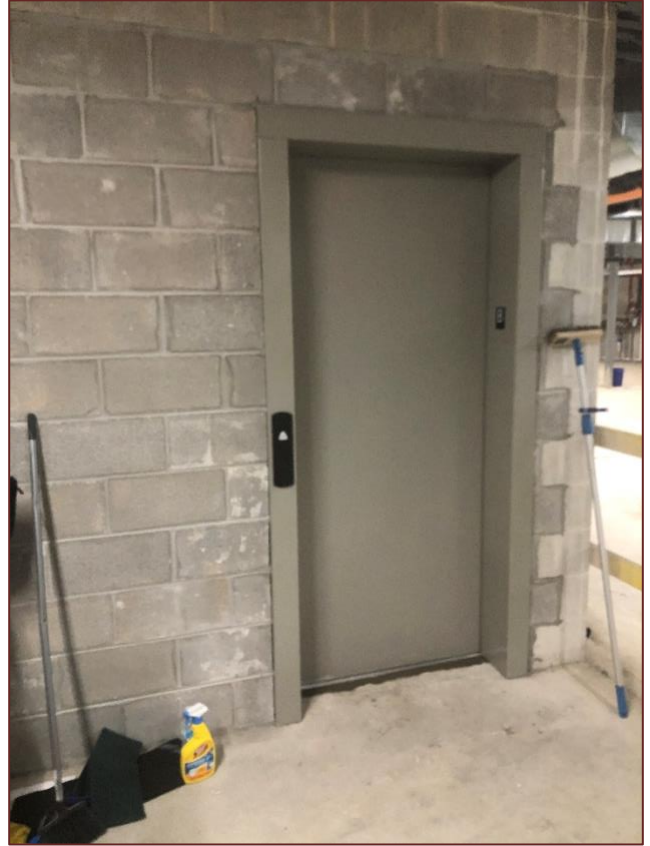

The Elevator.




Cleaning the Basement.

# The Township Center Project - 2020



The Food Pantry.

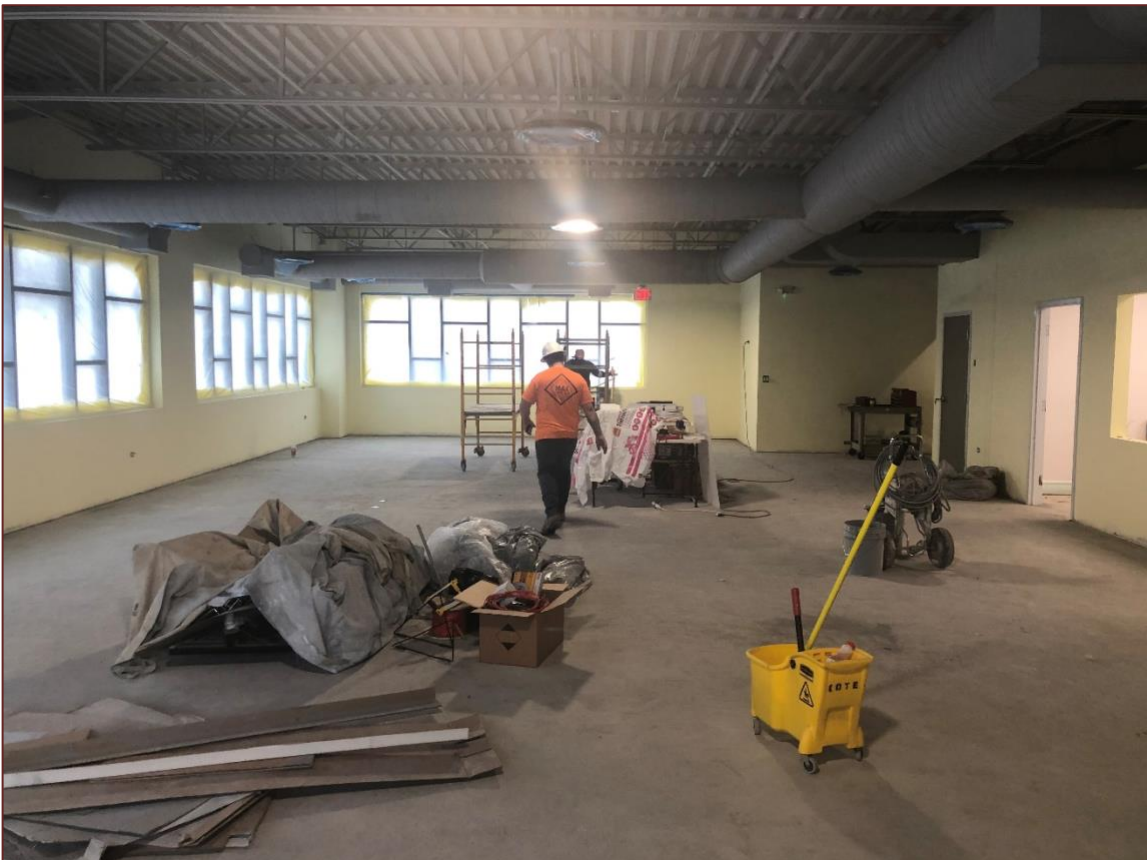

The Township Room.
