



The Township Center Project - 2020



SUBJECT: DAILY DIARY December 30, 2020

WEATHER: 20's degrees. Snowy.

WORK DAY = TODAY = $136 + 1 = 137$.

EP DOYLE: Graham.

CALIBER: +3.

TALON: +1.

PREMIUM [LCI CONCRETE] : +1.

HARD ROCK: +1.

PAINTER: +1.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today :

- Caliber working on completion of drywall sanding.
- Paint the hallway.
- Work on the trash enclosure.
- Breakout the failed concrete in the kitchen.
- Work on electrical details.

Activities Planned for Thursday.

- Paint the hallway and bathrooms.
- Clean up before painting the main rooms.
- Repair the kitchen floor.
- Complete the trash enclosure.

Critical Path:


- **Deliver and Install the Elevator.**

Pending Items:

-

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.

The Township Center Project - 2020

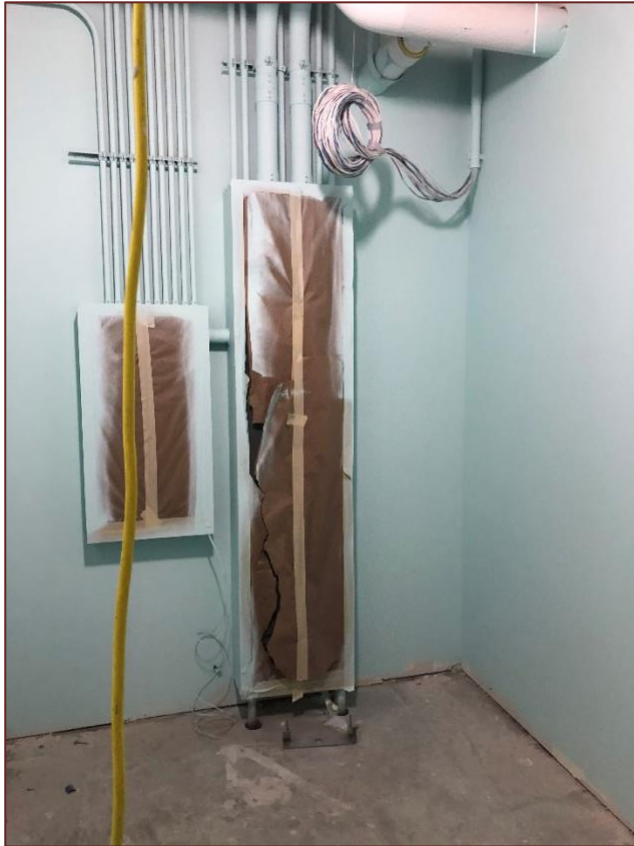

Painting today.



Working on the kitchen floor.



Working on the trash enclosure.

The Township Center Project - 2020



Main rooms to be cleaned before painting begins.
