



The Township Center Project - 2020



SUBJECT: DAILY DIARY: January 29, 2021

WEATHER: 10's degrees. Sunny.

WORK DAY = TODAY = 157 + 1 = 158.

EP DOYLE: Graham

TALON: +2.

PAINTER: + 1.

SIGNING: +2.

SCHINDLER: +0.

CLEANERS: +2.

CALIBER: +2.

WEBSTER McGRATH: +1.

ENGINEERING SOLUTIONS TEAM: Ed on-site.

Activities Today :

- Painting the Doors.
- Complete electrical details – inside and out.
- Install the window sills.
- Install the signing.
- Cleaning the building.
- Complete the Site As-Built Drawings.
- FINAL Village Inspection – PASSED.
- FINAL Village Fire Inspection – PASSED.

Activities Planned for Monday..

- Owner's Final Inspection.
- Architect's Building Commissioning.
- Final Elevator Inspection.


Pending Items:

- Inspections and Commissioning scheduled for February 1.
- Complete the RDA Document for Mark.

Thank you. Notes by Ed Kalina. / Please advise if there are any further thoughts or questions.



Installing the outside lighting.

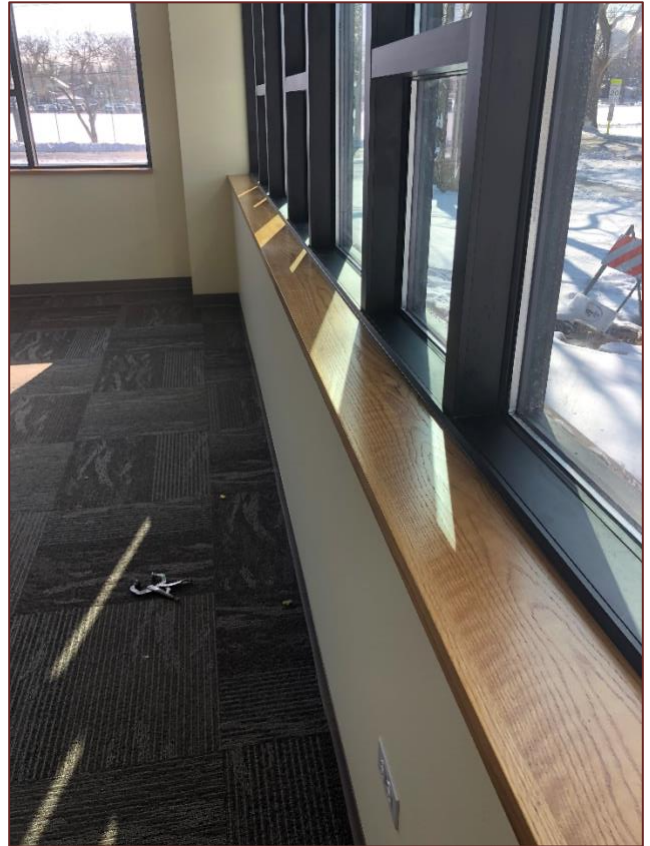

Window Sills.



Our host.



Hallway.

The Township Center Project - 2020



The Basement.



The Township Room.

The Township Center Project - 2020



The Kitchen.

